18

SINGLE SOURCE AWARD **BID # SS-11568-22**

Subject: Geo-Redundant Backup Solution for the First Coast Radio System (FCRS)

Department: Information Technologies Division

Description of Purchase:
Recommend approval to amend description of services with Motorola Solutions, Inc. for the purchase of Geo-Redundant Backup Solution for the First Coast Radio System (FCRS).
The purpose of this change order is to implement the following design and contract adjustments; Change location of the Master Prime site from JEA Plaza to Ed Ball (previously Cecil), Change locations of the new Dynamic Site Resilience (DSR) Master and Geo-Prime site at Cecil Field (previously Ed Ball), Update payment schedule to reflect changes to project milestones, Update the design and equipment to enable the switch to a Virtual Prime solution, and Add on-site training for Virtual Prime solution architecture. The period of service will remain the same until the date of final project acceptance, expiration of the warranty period, or completion of the services, whichever occurs last.

There will be no additional cost to the City and the total award remain the same. To be executed by formal contract amendment through the Office of General Counsel and process by purchase order(s).

Single Source Award To: Motorola Solutions, Inc.

Price Justification: See Attached

Total Award: $4,351,999.00 **Requisition #** FAIT-501569-22

Attachments: Agency Memo, Vendor Change Order, Previous Award

Certification as to Single Source: Kenneth Lathrop, Chief of Information Technologies Division/CIO

THE ABOVE PURCHASE IS RECOMMENDED FOR AWARD IN ACCORDANCE WITH CHAPTER 126.206.

ANALYST: Ruben Ola

Gregory Pease, Chief
Procurement Division

APPROVAL OF GENERAL GOVERNMENT AWARDS COMMITTEE
"ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS"

CHAIRMAN ***DATE***

ACTION OF AWARDING AUTHORITY

DATE: _____

APPROVED _____ **DISAPPROVED** _____

OTHER _____

SIGNATURE OF AUTHENTICATION _____

FORM GB-114, Revised 12/2007

INFORMATION TECHNOLOGIES DIVISION

CITY OF JACKSONVILLE

DATE: March 11, 2022

TO: Greg Pease, Chief of Procurement Division

THRU: Kenneth E. Lathrop, Chief of Information Technologies / CIO

Kenneth E. Lathrop — Digitally signed by Kenneth E. Lathrop Date: 2022.03.14 10:30:38 -04'00'

FROM: Thomas Ossi, Technology Contract and Records Manager

THOMAS OSSI — Digitally signed by THOMAS OSSI Date: 2022.03.14 09:43:55 -04'00'

RE: **SS-11568-22 Motorola Solutions – Change Order #1 for Geo-Redundant Master Prime (GRMP) First Coast Radio System Project**

The Information Technologies Division (ITD) requests approval for zero-dollar Change Order #1 for the Geo-Redundant Master Prime site project for the First Coast Radio System (FCRS) from Motorola Solutions, Inc. (Motorola).
The purpose of this change order is to implement the following design and contract adjustments:

- Change location of the Master Prime site from JEA Plaza to Ed Ball (previously Cecil)
- Change locations of the new Dynamic Site Resilience (DSR) Master and Geo-Prime site at Cecil Field (previously Ed Ball)
- Update payment schedule to reflect changes to project milestones
- Update the design and equipment to enable the switch to a Virtual Prime solution
- Add on-site training for Virtual Prime solution architecure

Change Order #1 will require an amendment to contract # 71498-22 through the Office General Counsel.

The total not-to-exceed amount for this request is $0.00.

Tracy Geake — Digitally signed by Tracy Geake Date: 2022.03.14 09:53:11 -04'00'

FUNDING SOURCE: 32111.153103.565051.010339.00000000.00000

Your favorable consideration of ITD's request is appreciated.

Attachments: Motorola CO #1
City Contract #71498-22
SS-11568-22

CC: Alexander Ciprian, Radio Communications Manager
William J. Costa, Technology Infrastructure Manager
Pieter Jansen, Information Technology Sr. Project Manager

MOTOROLA SOLUTIONS	CHANGE ORDER No.: 1

Date:	March 10, 2022
Project Name:	Jacksonville Geo-Redundant Master Prime
Customer Name:	City of Jacksonville
Customer Project Mgr:	Pieter Jansen
Motorola Project Manager:	Eric Lazo

The purpose of this Change Order:

This change order is to take into account the request from the City of Jacksonville to locate the equipment as follows:

- Install the Master and Prime from JEA Plaza to Ed Ball
- Install the new DSR Master and Geo-Prime at Cecil Field

This change order will also take into account installing a new Virtual Prime solution at both Ed Ball and Cecil Field.

Motorola Contract No.	FL-17I125A	**Contract Date:**	12/16/21
Customer Contract No.	**71498-22**		

In accordance with the terms and conditions of the Contract identified above between Motorola Solutions, Inc. and the City of Jacksonville, the following changes are approved:

1. Contract Price Adjustments

Original Contract Value:	$3,957,999.00
Previous Change Order amounts for Change Order numbered N/A through N/A	$ 0.00
This Change Order:	$ 0.00
New Contract Value:	$3,957,999.00

2. Completion Date Adjustments

Original Completion Date:	10/2/2023
Current Completion Date prior to this Change Order:	10/2/2023
New Completion Date:	10/2/2023

MOTOROLA SOLUTIONS	CHANGE ORDER No.: 1

3. Changes in Equipment *(additions, deletions or modifications)*

New City of Jacksonville System Layout as follows:

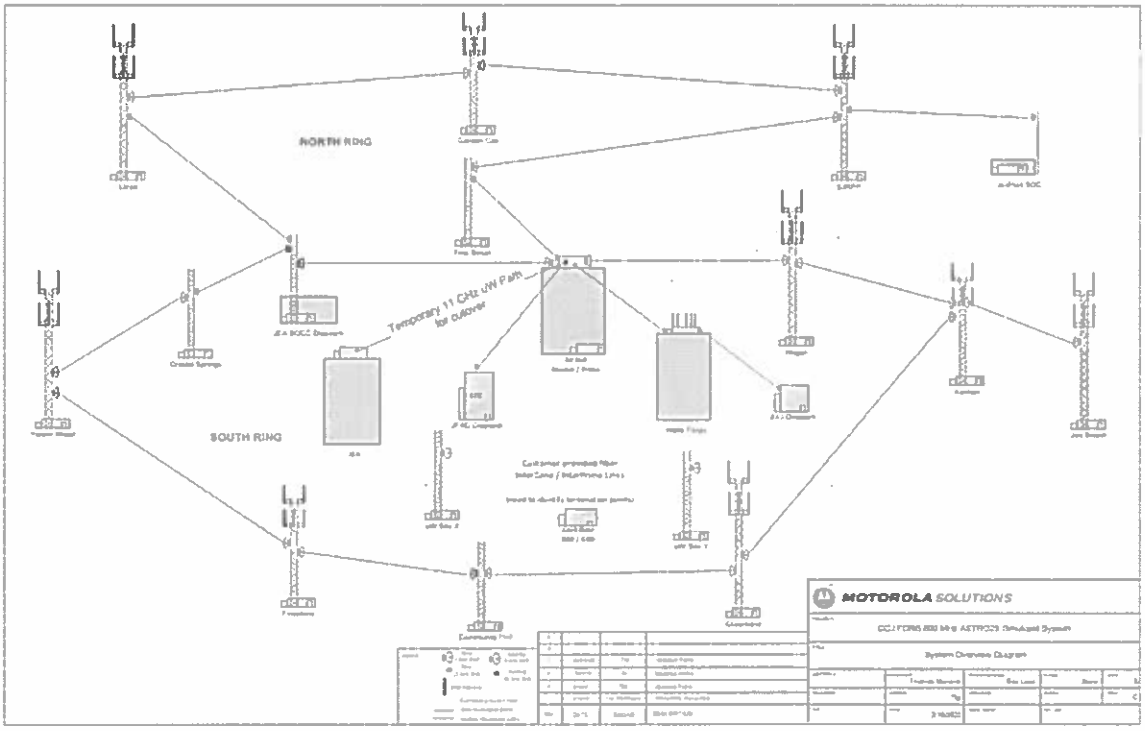

The current executed contract states that the existing Master and Prime Sites would be relocated to Cecil Field with the new DSR and Geo-Prime to be installed at the Ed Ball Building. This change order approves installing the existing Master and Prime sites at the Ed Ball Building with the new DSR and Geo-Prime being installed at Cecil Field. Due to space constraints at Cecil Field, and in order to accommodate the City of Jacksonville's request to relocate the equipment, we have proposed a Virtual Prime Solution which will take up a smaller footprint than the original proposed design.

Equipment deletions from the executed contract are as follows:

Section 9.1, DSR Geo Prime, Items 1 - 80

Equipment additions due to the Virtual Prime solution are as follows:

See Exhibit A

4. Changes in Services *(additions, deletions or modifications)*

A Virtualized Simulcast Prime Site Training Workshop to be held onsite in Jacksonville, FL.

5. Project Schedule Changes *(additions, deletions or modifications)*

No project schedule changes.

MOTOROLA SOLUTIONS	CHANGE ORDER No.: 1

6. Pricing Changes *(additions, deletions or modifications)*

No pricing changes.

7. Customer Responsibilities *(additions, deletions or modifications)*

The City of Jacksonville will need to provide 2 fiber links at Cecil Field to two different City of Jacksonville Tower Sites in order to tie into the Microwave Network.

8. Payment Schedule *(additions, deletions or modifications)*

Modification in milestone payment description, no changes to the milestone % as follows:

Cutover of DSR and Virtual Geo Prime (Cecil Field)	Jan 2023	25%	$989,500
Prime Site Relo to Ed Ball/System Acceptance	Jan 2023	23%	$910,340

Motorola Solutions, Inc.

By: Michael Harry

Printed Name: Michael Harry

Title: Systems Integration Manager

Date: March 10, 2022

Customer: City of Jacksonville, FL

By:

Printed Name:

Title:

Date:

DocuSign Envelope ID: 9D999ABB-38BE-4739-8AAA-665DEDB7C0EB

EXHIBIT A

DocuSign

Certificate Of Completion

Envelope Id: 9D999ABB38BE47398AAA665DEDB7C0EB
Subject: Please DocuSign: COJ GRMP Change Order 1.doc
Source Envelope:
Document Pages: 4
Certificate Pages: 1
AutoNav: Enabled
EnvelopeId Stamping: Enabled
Time Zone: (UTC-06:00) Central Time (US & Canada)

Signatures: 1
Initials: 0

Status: Completed

Envelope Originator:
Eric Lazo
500 West Monroe
Chicago, IL 60661
eric.lazo@motorolasolutions.com
IP Address: 73.148.246.192

Record Tracking

Status: Original
3/10/2022 8:48:31 AM

Holder: Eric Lazo
eric.lazo@motorolasolutions.com

Location: DocuSign

Signer Events	Signature	Timestamp
Michael Harry m.harry@motorolasolutions.com System Integration Manager Motorola Solutions, Inc. Security Level: Email, Account Authentication (None) **Electronic Record and Signature Disclosure:** Not Offered via DocuSign	Michael Harry Signature Adoption: Pre-selected Style Using IP Address: 174.209.202.110 Signed using mobile	Sent: 3/10/2022 8:57:27 AM Viewed: 3/10/2022 9:17:20 AM Signed: 3/10/2022 9:17:31 AM

In Person Signer Events	Signature	Timestamp

Editor Delivery Events	Status	Timestamp

Agent Delivery Events	Status	Timestamp

Intermediary Delivery Events	Status	Timestamp

Certified Delivery Events	Status	Timestamp

Carbon Copy Events	Status	Timestamp

Witness Events	Signature	Timestamp

Notary Events	Signature	Timestamp

Envelope Summary Events	Status	Timestamps
Envelope Sent	Hashed/Encrypted	3/10/2022 8:57:27 AM
Certified Delivered	Security Checked	3/10/2022 9:17:20 AM
Signing Complete	Security Checked	3/10/2022 9:17:31 AM
Completed	Security Checked	3/10/2022 9:17:31 AM

Payment Events	Status	Timestamps

SINGLE SOURCE AWARD **BID # SS-11568-22**

Subject: Geo-Redundant Backup Solution for the First Coast Radio System (FCRS)

Department: Information Technologies Division

Description of Purchase:
Recommend approval of Single Source Award to Motorola Solutions, Inc. for the purchase of Geo-Redundant Backup Solution for the First Coast Radio System (FCRS). FCRS is the primary method of communication for the Jacksonville Sheriff's Office (JSO), the Jacksonville Fire and Rescue Department (JFRD), and other local public safety subscribers. The backup system will include Dynamic System Resilience and a Geo-Redundant Prime site. The period of service will begin on the effective date of the contract and continue until the date of final project acceptance, expiration of the warranty period, or completion of the services, whichever occurs last. Total requested expenditure not to exceed $4,351,999.00.

Funding Source: 32111.153103.565051.010339.00000000.00000.0000000, to be executed by formal contract through the Office of General Counsel and process by purchase order(s).

Single Source Award To: Motorola Solutions, Inc.

Price Justification: See Attached

Total Award: $4,351,999.00 **Requisition #** FAIT-501137-22

Attachments: Single Source Form; Agency Memo, Vendor Letter, Vendor Quote

Certification as to Single Source: Kenneth Lathrop, Chief of Information Technologies Division/CIO

THE ABOVE PURCHASE IS RECOMMENDED FOR AWARD IN ACCORDANCE WITH CHAPTER 126.206.

ANALYST: Ruben Ola

Gregory Pease, Chief
Procurement Division

APPROVAL OF GENERAL GOVERNMENT AWARDS COMMITTEE

"ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS"

CHAIRMAN

DATE 11/18/2021

ACTION OF AWARDING AUTHORITY

DATE: 11/19/2021

APPROVED ✓ DISAPPROVED

OTHER

SIGNATURE OF AUTHENTICATION

Brian Hughes
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of:
Executive Order No: 2019-02

FORM GB-114, Revised 12/2007

Requisition FAIT-501569-22

Requisitioning BU FAIT: Information Technologies
Entered By Andre Conyers
Status Approved
Description SS-11568-22 Motorola Geo-Redundant Master Prime Site - Change Order #1. Amendment 1 to contract #71498-22 is a zero-dollar change order to change locations, update payment schedule, update the design and equipment, and add on-site training.
Emergency Requisition No

Requisition Amount 0 USD
Justification
Funds Status Reserved

Attachments

Title	File Name or URL	Description
FW_ SS-11568-22 Motorola Geo-R	FW_ SS-11568-22 Motorola Geo-Redundant Master Prime Site - Change Order #1.pdf	
Motorola GRMP CO #1 3-10-22.pd	Motorola GRMP CO #1 3-10-22.pdf	
SS-11568-22 GGAC AWARD. MOTORO	SS-11568-22 GGAC AWARD. MOTOROLA FCRS.pdf	
GC-#1472735-v1-Motorola_Soluti	GC-#1472735-v1-Motorola_Solutions_Inc_#71498-22_Communications_System_and_Services_Agreement.PDF	
Motorola GRMP CO 1 Memo 0311 2	Motorola GRMP CO 1 Memo 0311 2022 v1 (1)_.pdf	

Lines

Line	Item	Description	Category Name	Quantity	UOM	Price	Amount (USD)	Status	Funds Status
1		SS-11568-22 Motorola Geo-Redundant Master Prime Site - Change Order #1. Amendment 1 to contract #71498-22 is a zero-dollar change order to change locations, update payment schedule, update the design and equipment, and add on-site training.	992.71 Radio Instrument Testing and Calibration Services	1	Each	0.00 USD	0	Approved	Reserved

Requester Alexander Ciprian
Urgent No
Requested Delivery Date 3/28/22
Deliver-to Location Communications Facility

Supplier Motorola Solutions, Inc.
Supplier Site Ordering
Supplier Contact Michelle Poole
Contact Phone

Requisition FAIT-501569-22

Deliver-to Address	Charge 1020 Superior Street, Jacksonville, FL 32254, Duval, United States	**Charge Account**	32111.153103.565051.010339.00000000.00000.0000000
Note to Buyer			

I CERTIFY THAT FUNDS FOR THIS PURCHASE WERE AUTHORIZED AND PROVIDED FOR IN THE CURRENT BUDGET.
