23

SUBJECT: RFQ-DESIGN-BUILD SERVICES FIRE STATIONS NUMBERS: 36, 64, AND 65

BID # CDB-0127-19 **OPEN DATE: 2019-04-17**

COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT: CONSTRUCTION – DESIGN/BUILD- REQUEST FOR QUALIFICATIONS

AGENCY: DEPARTMENT OF PUBLIC WORKS

BASIS OF AWARD: EVALUATION CRITERIA

NUMBER OF BIDS INVITED: 5 **NUMBER RECEIVED: 6** **OTHER: 0**

SUMMARY OF BIDS AND RECOMMENDED ACTIONS:

Recommend approval of Amendment 1 to Stellar Group, Inc. to provide 100% design, permits, and construction services for Fire Station No. 65 in the amount of $4,889,907.00 which includes $211,122.00 in contingency. This incorporates the scope & fee summary, Exhibit "B" and allows for a completion date of 317 calendar days from the Notice to Proceed. Total guaranteed maximum price not-to-exceed $5,131,216.11.

Funding for this award is to be encumbered by account: 004335.565051.1.32111.384020 to be executed by contract amendment through Office of General Counsel.

ATTACHMENTS: Recommendation Memo, Exhibit "B", Previous Award(s)

ANALYST: _____
BRYAN MATUS

RESPECTFULLY SUBMITTED: _____
GREGORY PEASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: **Robin G. Smith, P.E., Chief, Engineering and Construction Management**

(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING_____ MEMBERS DISAPPROVING_____ DATE:_____

_____ _____ OTHER_____

_____ _____

_____ _____

_____ _____

_____ _____

ACTION OF AWARDING AUTHORITY DATE _____

APPROVED_____ DISAPPROVED: _____

OTHER: _____

SIGNATURE OF AUTHENTICATION _____

City of Jacksonville, Florida

Lenny Curry, Mayor

Department of Public Works
Engineering & Construction Management Division
214 N. Hogan Street, 10th Floor
Jacksonville, FL 32202
(904) 255-8762
www.coj.net

ONE CITY ONE JACKSONVILLE

November 24, 2021

TO: Gregory W. Pease
Chief of Procurement

THRU: John P. Pappas, P.E.
Director

FROM: Robin G. Smith, P.E.
Chief, Engineering and Construction Management Division

Keith Powers
Director of Fire and Rescue

SUBJECT: Design Build Services for Fire Station 65
Stellar Group, Inc. Contract 71001-21 PO # 622504-21

In accordance with Design/Build CDB-0127-19, Contract 71001-21 for Fire Station #65 was awarded in the amount of $241,309.11 to provide 90% Design and Preconstruction Services. Amendment 1 is to provide 100% design, permits and construction services, as indicated on the attached Scope & Fee Summary, Exhibit B in the amount of $4,889,907.00, which includes $211,122.00 in contingency and allowing for 317 calendar days from the Notice to Proceed.

Accordingly, this is to recommend that Contract 71001-21, originally executed August 9, 2021, with Stellar Group, Inc. for Fire Station No. 65 be amended to incorporate the attached Scope and Fee, Exhibit B to increase the GMP by $4,889,907.00 to a new GMP of $5,131,216.11.

Funding is as follows:

Accounts	TOTAL
004335	
FRCP Fire Stations Capital Projects- Fire Control	
565051	
1	
32111-384020	
$4,889,907.00	$4,889,907.00

RGS/lw

Cc: Maria Williams, Engineering and Construction Management
Lori West, Engineering and Construction Management
Rich Cooper, Engineering and Construction Management

Attachment: Exhibit B - Scope & Fee Summary

88

stellar | TAKING SOLUTIONS FURTHER®

City of Jacksonville - Fire Station 65

90% Design Document Deliverable

November 5, 2021

PLANNING | DESIGN | PRE-CONSTRUCTION | CONSTRUCTION | REFRIGERATION | MECHANICAL & UTILITY | BUILDING ENVELOPE | TOTAL OPERATIONS & MAINTENANCE



stellar | TAKING SOLUTIONS FURTHER®

City of Jacksonville
Fire Station 65

90% Design Document Deliverable

November 5, 2021

Table of Contents

I. GMP Budget based on 90% Design Documents

II. Assumptions and Clarifications

III. Project Documents

IV. Project Schedule

V. Supporting Documents

- Construction Cost Inflation Report
- Good Faith Effort Bid Solicitations
- Public Bid Advertisement

© Stellar 2014

stellar | TAKING SOLUTIONS FURTHER®

GMP Budget based on 90% Design Documents

© Stellar 2014

EXHIBIT B

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
NUMBER: PROJECT NUMBER

SITE AREA (AC): 3.06
BUILDING AREA (GSF): 9,390

CITY OF JACKSONVILLE FIRE STATION NO. 65

SITE		$	1,211,537	$	395,500
BUILDING		$	3,010,905	$	320.65
BUILDING PERMIT/APPROVAL (ALLOWANCE)			Included		
	SUBTOTAL	$	4,222,442		
CONTINGENCY ON CONSTRUCTION COST	5.00%	$	211,122		
	SUBTOTAL	$	4,433,564		
PERFORMANCE & PAYMENT BOND	0.75%	$	36,007		
BUILDERS RISK INSURANCE	0.30%	$	14,410		
GENERAL LIABILITY	1.65%	$	79,256		
	SUBTOTAL	$	4,563,237		
PRECONSTRUCTION FEE	0.00%	$	-		
CONSTRUCTION FEE	5.00%	$	240,170		
TOTAL CONSTRUCTION BUDGET		**$**	**4,803,407**	**$**	**511.54**
FLORIDA GREEN BUILDING CONSULTING SERVICES		$	10,000		
FUNDAMENTAL COMMISSIONING		$	9,000		
REMAINING 10% CIVIL DESIGN FEES		$	30,000		
REMAINING 10% ARCHITECTURAL/MEP DESIGN FEES		$	37,500		
OVERALL DESIGN AND CONSTRUCTION BUDGET		**$**	**4,889,907**	**$**	**520.76**

stellar
TAKING SOLUTIONS FURTHER

STELLAR

DATE:	**November 5, 2021**	**SITE AREA:**	**3.06 AC**
PROJECT:	**COJ FIRE STATION No. 65**	**MO:**	**8**
PROJ NUM:	**PROJECT NUMBER**	**WK:**	**35**

SITEWORK

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST		BUDGET
30	SITE EXCAVATION AND GRADING				$	369,305
31	SITE PAVING				$	99,788
32	SITE DEVELOPMENT				$	121,170
33	LANDSCAPING				$	110,603
34	SITE UTILITIES				$	323,521
35	SITE ELECTRICAL				$	187,150
				SUBTOTAL	$	1,211,537
	CONTINGENCY ON CONSTRUCTION COST	5.00%			$	60,577
				SUBTOTAL	$	1,272,113
	P&P BOND	0.75%			$	10,331
	BUILDERS RISK	0.30%			$	4,135
	GENERAL LIABILITY	1.65%			$	22,741
				SUBTOTAL	$	1,309,320
	PRECONSTRUCTION FEE	0.00%			$	-
	CONSTRUCTION FEE	5.00%			$	68,912
				TOTAL SITE CONSTRUCTION BUDGET:	**$**	**1,378,232**

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

SITE AREA: 3.06 AC
MO: 8
WK: 35

SITEWORK

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY		UNIT COST		BUDGET
	SITEWORK						
30	**SITE EXCAVATION AND GRADING**						
31 20 00	MOBILIZATION		0	$	0.00		INCLUDED
31 20 00	SURVEYING AND LAYOUT		0	$	0.00		INCLUDED
31 20 00	TRAFFIC CONTROL		0	$	0.00		INCLUDED
31 20 00	DEWATERING		0	$	0.00		INCLUDED
31 20 00	TESTING AND ENGINEERING		0	$	0.00		INCLUDED
31 20 00	EROSION CONTROL		0	$	0.00		INCLUDED
31 20 00	SILT FENCE		0	$	0.00		INCLUDED
31 20 00	INLET PROTECTION		0	$	0.00		INCLUDED
31 20 00	CONSTRUCTION DRIVEWAY		0	$	0.00		INCLUDED
31 20 00	EROSION CONTROL MAINTENANCE		0	$	0.00		INCLUDED
31 20 00	SITE DEMOLITION		0	$	0.00		INCLUDED
31 20 00	CLEARING AND GRUBBING		0	$	0.00		INCLUDED
31 20 00	STRIP AND STOCKPILE TOPSOIL		0	$	0.00		INCLUDED
31 20 00	IMPORT FILL		0	$	0.00		INCLUDED
31 20 00	MASS GRADE AND BALANCE SITE		0	$	0.00		INCLUDED
31 20 00	CONSTRUCT NEW BUILDING PAD		0	$	0.00		INCLUDED
31 20 00	12" STABILIZATION		0	$	0.00		INCLUDED
31 20 00	4" BASE AT CONRETE PAVING		0	$	0.00		INCLUDED
31 20 00	FINE GRADING AT PAVING		0	$	0.00		INCLUDED
31 20 00	FINISH GRADING		0	$	0.00		INCLUDED
31 20 00	EARTHWORK AND SIT PREP	LS	1	$	369,305	$	369,305
	TOTAL SITE EXCAVATION AND GRADING					$	369,305
31	**SITE PAVING**						
32 12 00	ASPHALT PAVING 8" + 2"		0	$	0.00		INCLUDED
32 13 00	CONCRETE CURB & GUTTER - CITY STANDARD		0	$	0.00		INCLUDED
32 13 00	WALKS AND SLABS 4"		0	$	4.20		INCLUDED
32 13 00	CONCRETE ENTRANCE AND PATIO 4" SOG		0	$	6.76		INCLUDED
32 13 00	CONCRETE PADS 8"		0	$	10.77		INCLUDED
32 13 00	CONCRETE PAVING 8"-10" - APRON		0	$	12.60		INCLUDED
05 50 00	8" STEEL PROTECTION BOLLARDS - EXTERIOR		0	$	0.00		INCLUDED
32 13 00	ADA SIDEWALK RAMP		0	$	0.00		INCLUDED
32 13 00	ADA WARNING PAD (TRUNCATED DOME) 2'X2'		0	$	0.00		INCLUDED
32 13 00	SITE CONCRETE	LS	1	$	99,030	$	99,030
32 13 00	24"Ø LIGHT POLE BASES		0	$	0.00		INCLUDED
32 13 00	24"Ø FLAG POLE BASE		1	$	652.40	$	652

stellar
TAKING SOLUTIONS FURTHER

STELLAR

DATE:	**November 5, 2021**	**SITE AREA:**	**3.06 AC**
PROJECT:	**COJ FIRE STATION No. 65**	**MO:**	**8**
PROJ NUM:	**PROJECT NUMBER**	**WK:**	**35**

SITEWORK

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY		UNIT COST		BUDGET
32 17 23	PAVEMENT MARKING AND SIGNAGE		0	$	0.00		INCLUDED
32 17 23	PAVEMENT MARKING - HC PARKING	EA	2	$	52.55	$	105
	TOTAL SITE PAVING					$	99,788
32	**SITE DEVELOPMENT**						
03 00 00	WF4.0 - TRASH ENCL. CONTINUOUS FDN. - 1'x4'		0	$	0.00		INCLUDED
04 20 00	8" CMU - TRASH ENCLOSURE WALLS - 8'H		0	$	0.00		INCLUDED
04 20 00	PRECAST CAP - TRASH SCREEN/ENCL. WALLS		0	$	0.00		INCLUDED
32 30 00	TRASH ENCLOSURE GATES		0	$	0.00		INCLUDED
03 00 00	WF2.0 - STORAGE AREA CONTINUOUS FDN. - 1'x2'		0	$	0.00		INCLUDED
04 20 00	8" CMU - STORAGE ENCLOSURE WALLS - 10'-8"H		0	$	0.00		INCLUDED
08 20 00	STORAGE ENCLOSURE DOORS - SEE BUILDING		0	$	0.00		INCLUDED
07 30 00	COMPOSITION SHINGLES - STORAGE/EXTRACTOR		0	$	0.00		INCLUDED
07 30 00	METAL FASCIA W/DRIP - STORAGE/EXTRACTOR		0	$	0.00		INCLUDED
09 24 00	STUCCO ON CMU SCREEN/ENCLOSURE WALLS		0	$	0.00		NOT REQ'D
32 31 00	CHAIN LINK FENCING, 6'		0	$	0.00		INCLUDED
32 31 00	CHAIN LINK FENCING, 8'		0	$	0.00		INCLUDED
32 31 00	MOTORIZED DRIVE GATE PREMIUM		0	$	0.00		INCLUDED
32 31 00	SWING GATE, MANUAL		0	$	0.00		INCLUDED
32 31 00	PRIVACY SLATS		0	$	0.00		INCLUDED
32 31 00	CHAIN LINK FENCING AND GATES	LS	1	$	110,700	$	110,700
10 14 00	MONUMENT SIGN - ALLOWANCE		0	$	0.00		NOT REQ'D
10 75 00	FLAGPOLES	EA	1	$	10,470	$	10,470
09 90 00	PAINT BOLLARDS		0	$	0.00		NOT REQ'D
	TOTAL SITE DEVELOPMENT					$	121,170
33	**LANDSCAPING**						
32 90 00	LANDSCAPING AND IRRIGATION	LS	1	$	110,603	$	110,603
	TOTAL LANDSCAPING					$	110,603
34	**UTILITIES**						
33 00 00	18"Ø RCP STORM SEWER		0	$	0.00		INCLUDED
33 00 00	24"Ø RCP STORM SEWER		0	$	0.00		INCLUDED
33 00 00	INLETS & JUNCTION BOXES		0	$	0.00		INCLUDED
33 00 00	48"Ø MANHOLE		0	$	0.00		INCLUDED
33 00 00	24" MES OUTLET STRUCTURE		0	$	0.00		INCLUDED
33 00 00	POND UNDERDRAIN - 6" PERF. ADS PIPE		0	$	0.00		INCLUDED
33 00 00	RETENTION POND		0	$	0.00		INCLUDED

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

SITE AREA: 3.06 AC
MO: 8
WK: 35

SITEWORK

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY		UNIT COST		BUDGET
33 00 00	6" SDR 35 SANITARY SEWER		0	$	0.00		INCLUDED
33 00 00	6" SDR 18 SANITARY SEWER		0	$	0.00		INCLUDED
33 00 00	PVC FITTINGS AND CLEANOUTS		0	$	0.00		INCLUDED
33 00 00	LIFT STATION		0	$	0.00		INCLUDED
33 00 00	SANITARY SEWER PUMP-OUT MANHOLE ASSEMBLY		0	$	0.00		INCLUDED
33 00 00	CITY SEWER - CONNECT TO EXISTING SERVICE		0	$	0.00		INCLUDED
33 00 00	DOMESTIC WATER SERVICE - 1.5" POLYETHYLENE		0	$	0.00		INCLUDED
33 00 00	CITY WATER SERVICE - 8" DR18		0	$	0.00		INCLUDED
33 00 00	FIRE WATER SERVICE 6" DR18		0	$	0.00		INCLUDED
33 00 00	FIRE HYDRANT		0	$	0.00		INCLUDED
33 00 00	METER BOX		0	$	0.00		INCLUDED
33 00 00	8" BACKFLOW PREVENTER		0	$	0.00		INCLUDED
33 00 00	CITY WATER - CONNECT TO EXISTING SERVICE		0	$	0.00		INCLUDED
33 00 00	FIRE PERMIT AND TESTING		0	$	0.00		INCLUDED
33 00 00	STREET CROSSINGS		0	$	0.00		INCLUDED
33 00 00	SITE UTILITIES	LS	1	$	323,521	$	323,521
	TOTAL UTILITIES					$	**323,521**
35	**SITE ELECTRICAL**						
33 70 00	TELEPHONE & POWER CONDUITS		0	$	0.00		INCLUDED
33 70 00	LED SITE LIGHTING POLE - PARKING AND DRIVEWAY		0	$	0.00		INCLUDED
33 70 00	LIGHTING CONDUIT & WIRE, 1" PVC		0	$	0.00		INCLUDED
33 70 00	SITE ELECTRICAL	LS	1	$	187,150	$	187,150
	TOTAL SITE ELECTRICAL					$	**187,150**

stellar
TAKING SOLUTIONS FURTHER

STELLAR		MAIN LEVEL:	9,390
DATE:	November 5, 2021	2ND LEVEL:	0
PROJECT:	COJ FIRE STATION No. 65	TYP LEVEL:	0
PROJ NUM:	PROJECT NUMBER	NUM TYP LVLS:	0
		GROSS SQ.FT:	9,390
		MO	8
		WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
01	GENERAL CONDITIONS				$ 347,200	$ 36.98
02	DEMOLITION				$ -	$ -
03	STRUCTURAL EXCAVATION AND FOUNDATIONS				$ 152,440	$ 16.23
04	SUPERSTRUCTURE				$ 41,815	$ 4.45
05	ENCLOSURE				$ 341,540	$ 36.37
06	ROOFING AND SHEET METAL				$ 133,820	$ 14.25
07	ROUGH CARPENTRY				$ 323,209	$ 34.42
08	FINISH CARPENTRY				$ 59,510	$ 6.34
09	THERMAL AND MOISTURE PROTECTION				$ 7,505	$ 0.80
10	DOORS FRAMES AND HARDWARE				$ 119,231	$ 12.70
11	PARTITIONS				$ 126,000	$ 13.42
12	FINISHES				$ 110,105	$ 11.73
13	SPECIALTIES				$ 62,076	$ 6.61
14	EQUIPMENT AND FURNISHINGS				$ 82,267	$ 8.76
15	SPECIAL CONSTRUCTION				$ -	$ -
16	VERTICAL TRANSPORTATION				$ -	$ -
17	FIRE PROTECTION				$ 60,280	$ 6.42
18	PLUMBING				$ 149,500	$ 15.92
19	HVAC				$ 315,660	$ 33.62
20	ELECTRICAL				$ 466,249	$ 49.65
21	SECURITY AND LIFE SAFETY				$ 70,000	$ 7.45
	JEA UTILITY FEES (ALLOWANCE)				$ 35,000	$ 3.73
	BUILDING PERMIT AND FEES (ALLOWANCE)				$ 7,500	$ 0.80
				SUBTOTAL	$ 3,010,905	$ 320.65
	CONTINGENCY ON CONSTRUCTION COST	5.00%			$ 150,545	$ 16.03
				SUBTOTAL	$ 3,161,450	$ 336.68
	P&P BOND	0.75%			$ 25,675	$ 2.73
	BUILDERS RISK	0.30%			$ 10,276	$ 1.09
	GENERAL LIABILITY	1.65%			$ 56,515	$ 6.02
				SUBTOTAL	$ 3,253,917	$ 346.53
	PRECONSTRUCTION FEE	0.00%			$ -	
	CONSTRUCTION FEE	5.00%			$ 171,259	$ 18.24
	TOTAL BUILDING CONSTRUCTION BUDGET:				$ 3,425,175	$ 364.77

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY		UNIT COST		BUDGET		COST/ SQ.FT.
	BUILDING								
1	**INDIRECT JOB COSTS**								
01 00 01	GENERAL CONDITIONS					$	347,200	$	36.98
	TOTAL INDIRECT JOB COSTS					$	347,200	$	36.98
2	**DEMOLITION**								
	TOTAL DEMOLITION					$	-	$	-
3	**STRUCTURAL EXCAVATION AND FOUNDATIONS**								
31 20 10	STRUCTURAL EXCAVATION		0	$	0.00		INCLUDED	$	-
03 31 00	DEWATERING		0	$	0.52		INCLUDED	$	-
03 31 00	FINE GRADING		0	$	0.16		INCLUDED	$	-
03 31 00	F8.4 - COLUMN/PAD FOOTINGS - 8'-0"x4'-0"x1'-6"		0	$	0.00		INCLUDED	$	-
03 31 00	F3.0 - COLUMN/PAD FOOTINGS - 3'-0"x3'-0"x1'-0"		0	$	0.00		INCLUDED	$	-
03 31 00	WF4.0 - CONTINUOUS WALL FOOTINGS BLDG - 4'x1'		0	$	0.00		INCLUDED	$	-
03 31 00	WF4.0 - CONTINUOUS WALL FOOTINGS SCREEN ' 4'x1'		0	$	0.00		INCLUDED	$	-
03 31 00	SLAB ON GRADE (4")		0	$	0.00		INCLUDED	$	-
03 31 00	SLAB ON GRADE (10")		0	$	0.00		INCLUDED	$	-
03 31 00	THICKENED SLAB EDGE		0	$	0.00		INCLUDED	$	-
03 31 00	BUILDING FOUNDATIONS AND SLABS ON GRADE	LS	1	$	152,440	$	152,440	$	16.23
03 31 00	TERMITE TREATMENT UNDER BUILDING SLAB		0	$	0.00		INCLUDED	$	-
	TOTAL STRUCTURAL EXCAVATION AND FOUNDATIONS					$	152,440	$	16.23
4	**SUPERSTRUCTURE**								
04 20 00	TIE BEAMS AT OVERHEAD DOORS		0	$	0.00		NOT REQ'D	$	-
05 50 00	8" STEEL PROTECTION BOLLARDS - INTERIOR		0	$	0.00		INCLUDED	$	-
05 50 00	MISCELLANEOUS STEEL/ANCHORING HARDWARE	LS	1	$	41,815	$	41,815	$	4.45
	TOTAL SUPERSTRUCTURE					$	41,815	$	4.45
5	**ENCLOSURE**								
04 20 00	SPLIT FACE CMU 8" - BLDG SCREEN WALL		0	$	0.00		INCLUDED	$	-
04 20 00	SPLIT FACED CMU 8" - LOAD BEARING		0	$	0.00		INCLUDED	$	-
04 20 00	SPLIT FACED CMU 12" - LOAD BEARING		0	$	0.00		INCLUDED	$	-
04 20 00	MASONRY PILASTERS		0	$	0.00		INCLUDED	$	-
04 20 00	MASONRY COLUMNS - COVERED PATIOS		0	$	0.00		INCLUDED	$	-
04 20 00	MASONRY	LS	1	$	294,000	$	294,000	$	31.31
08 40 00	EXTERIOR STOREFRONT		0	$	0.00		INCLUDED	$	-

stellar

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
08 40 00	PUNCH WINDOWS (TYPE A, B, C & E)		0	$ 0.00	INCLUDED	$ -
08 40 00	ALUMINUM ENT DOORS, 7 FEET TALL		0	$ 0.00	INCLUDED	$ -
01 10 02	FINAL GLASS CLEANING	SF	361	$ 0.54	$ 195	$ 0.02
08 40 00	GLASS AND GLAZING	LS	1	$ 47,345	$ 47,345	$ 5.04
	TOTAL ENCLOSURE				**$ 341,540**	**$ 36.37**
6	**ROOFING AND SHEET METAL**					
07 30 00	ARCHITECTURAL SHINGLES W/ICE AND WATER SHIELD	LS	1	$ 93,700	$ 93,700	$ 9.98
07 21 29	SPRAY FOAM INSULATION - UNDERSIDE OF ROOF	LS	1	$ 40,120	$ 40,120	$ 4.27
07 60 00	PREFINISHED BREAK METAL AT PERIM ROOF FASCIA		0	$ 0.00	INCLUDED	$ -
07 60 00	PREFINISHED BREAK METAL AT PATIO AND ENTRY		0	$ 0.00	INCLUDED	$ -
07 60 00	GUTTERS & DOWNSPOUTS		0	$ 0.00	INCLUDED	$ -
	TOTAL ROOFING AND SHEET METAL				**$ 133,820**	**$ 14.25**
7	**ROUGH CARPENTRY**					
06 10 00	WOOD PREFAB ROOF TRUSS FRAMING AND SHEATHING	SF	10,695	$ 22.86	$ 244,474	$ 26.04
06 10 00	SOFFIT FRAMING			$ 0.00	INCLUDED	$ -
06 10 10	FASCIA FRAMING			$ 0.00	INCLUDED	$ -
06 10 10	VINYL PANEL SOFFIT - NON-PERFORATED		0	$ 0.00	INCLUDED	$ -
06 10 10	METAL PANEL SOFFIT - PATIO ONLY		0	$ 0.00	INCLUDED	$ -
06 10 00	HOISTING FOR TRUSSES (80T RT)			$ 0.00	INCLUDED	$ -
06 10 10	BLOCKING AT DOORS			$ 0.00	INCLUDED	$ -
06 10 10	BLOCKING AT WINDOWS			$ 0.00	INCLUDED	$ -
06 10 10	BLOCKING AT CASEWORK/TRIM			$ 0.00	INCLUDED	$ -
06 10 10	PLYWOOD BACKING AT ELEC & COMM RMS			$ 0.00	INCLUDED	$ -
06 10 10	ROUGH CARPENTRY	SF	9,390	$ 8.38	$ 78,735	$ 8.38
	TOTAL ROUGH CARPENTRY				**$ 323,209**	**$ 34.42**
8	**FINISH CARPENTRY**					
06 20 00	PLAM VANITIES - MEN'S AND WOMEN'S BATHROOMS		0	$ 0.00	INCLUDED	$ -
06 20 00	SHELVING - EMS		0	$ 0.00	INCLUDED	$ -
06 20 00	SHELVING - STORAGE		0	$ 0.00	INCLUDED	$ -
06 20 00	SHELVING - STORAGE 110, 111, 112		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE BASE CABINETS - CHIEF ROOM		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE BASE CABINETS - DISPATCH		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE BASE CABINETS - PRIVATE		0	$ 0.00	INCLUDED	$ -
06 20 00	STAINLESS STEEL BASE CABINETS - KITCHEN				w/EQUIP & FURN	
06 20 00	PLASTIC LAMINATE COUNTERTOPS 24" - CHIEF ROOM		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE COUNTERTOPS 24" - DISPATCH		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE COUNTERTOPS 24" - PRIVATE		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE UPPER CABINETS - BUNKER		0	$ 0.00	INCLUDED	$ -

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
06 20 00	PLASTIC LAMINATE UPPER CABINETS - KITCHEN		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE UPPER CABINETS - LAUNDRY		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE UPPER CABINETS - CORRIDOR 114		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE LINEN CABINETS - M & W RR		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE LINEN CABINETS - TOILET RM 104		0	$ 0.00	INCLUDED	$ -
06 20 00	PLASTIC LAMINATE LINEN CABINETS - CHIEF ROOM		0	$ 0.00	INCLUDED	$ -
06 20 00	STORAGE SHELVING		0	$ 0.00	INCLUDED	$ -
06 20 00	BUNKER GEAR STORAGE CASEWORK		0	$ 0.00	INCLUDED	$ -
06 20 00	FINISH CARPENTRY	LS	1	$ 59,510	$ 59,510	$ 6.34
	TOTAL FINISH CARPENTRY				**$ 59,510**	**$ 6.34**
9	**THERMAL AND MOISTURE PROTECTION**					
07 92 00	BUILDING, DOOR & WINDOW CAULKING	SF	1,689	$ 1.20	$ 2,027	$ 0.22
07 92 00	CAULK CMU CONTROL JOINTS	LF	700	$ 3.60	$ 2,520	$ 0.27
07 92 00	INTERIOR CAULKING	SF	9,390	$ 0.32	$ 2,958	$ 0.32
	TOTAL THERMAL AND MOISTURE PROTECTION				**$ 7,505**	**$ 0.80**
10	**DOORS FRAMES AND HARDWARE**					
08 20 00	HOLLOW METAL FRAMES, WELDED		0	$ 0.00	INCLUDED	$ -
08 20 20	HOLLOW METAL DOORS		0	$ 0.00	INCLUDED	$ -
08 20 30	WOOD DOOR		0	$ 0.00	INCLUDED	$ -
08 70 00	FINISH HARDWARE		0	$ 0.00	INCLUDED	$ -
08 10 10	UNLOAD & DISTRIBUTE DR, FRAME, HDWE	EA	43	$ 31.50	$ 1,355	$ 0.14
08 10 10	SECURE HARDWARE STORAGE	EA	1	$ 850.00	$ 850	$ 0.09
08 20 30	DOORS FRAMES AND HARDWARE - FURNISH	LS	1	$ 65,973	$ 65,973	$ 7.03
08 10 10	DOORS, FRAMES, HARDWARE - INSTALL	LS	1	$ 9,067	$ 9,067	$ 0.97
08 30 00	NON-INSULATED SECTIONAL OH DOOR (14'x14')	LS	1	$ 41,986	$ 41,986	$ 4.47
08 30 00	OH DOOR SAFETY AND CONVENIENCE PKG		0	$ 0.00	INCLUDED	$ -
08 40 10	GLAZE SIDELITES & BORROW LITES		0	$ 0.00	INCLUDED	$ -
08 40 10	INT STOREFRONT DOORS		0	$ 0.00	INCLUDED	$ -
08 40 10	INT STOREFRONT DOORS		0	$ 0.00	INCLUDED	$ -
	TOTAL DOORS FRAMES AND HARDWARE				**$ 119,231**	**$ 12.70**
11	**PARTITIONS**					
08 40 10	INTERIOR STOREFRONT - 1/4" SINGLE GLAZING		0	$ 0.00	INCLUDED	$ -
09 20 00	TYPE 5 PARTITION - 3-5/8, LOW WALL				INCLUDED	$ -
09 20 00	TYPE 6 PARTITION - 3-5/8, 25GA, BATT INSUL				INCLUDED	$ -
09 20 00	TYPE 6B PARTITION - 3-5/8, 25GA, NO INSUL				INCLUDED	$ -
09 20 00	TYPE 6S PARTITION - 3-5/8, 25GA, 1HR				INCLUDED	$ -
09 20 00	TYPE 7 PARTITION - 3-5/8, KNEE WALL				INCLUDED	$ -
09 20 00	TYPE 9 PARTITION - 6", 25GA BATT INSUL				INCLUDED	$ -

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
09 20 00	TYPE 10 PARTITION - 6" 1-SIDE WALL - PLUMBING				INCLUDED	$ -
09 20 00	GWB FURRED ON CMU- 2-1/2"				INCLUDED	$ -
09 20 00	INTERIOR DRYWALL PARTITIONS	SF	LS	$ 1.00	$ 126,000	$ 13.42
	TOTAL PARTITIONS				**$ 126,000**	**$ 13.42**
12	**FINISHES**					
09 30 00	CERAMIC TILE FLOOR		0	$ 0.00	INCLUDED	$ -
09 30 00	TILE BASE		0	$ 0.00	INCLUDED	$ -
09 30 00	CERAMIC TILE WALLS		0	$ 0.00	INCLUDED	$ -
09 30 00	CERAMIC TILE BACKSPLASH - KITCHEN		0	$ 0.00	INCLUDED	$ -
09 30 00	CERAMIC TILE - FLOOR AND WALLS		0	$ 0.00	INCLUDED	$ -
03 35 00	POLISH, STAIN AND SEAL CONCRETE	LS	1	$ 29,880	$ 29,880	$ 3.18
09 60 00	SHEET RUBBER FLOORING		0	$ 0.00	INCLUDED	$ -
09 60 00	RESILIENT BASE, 4"		0	$ 0.00	INCLUDED	$ -
09 60 00	RUBBER FLOORING AND CERAMIC TILE	LS	1	$ 20,682	$ 20,682	$ 2.20
09 50 00	2X2 ACOUSTIC CEILINGS		0	$ 0.00	INCLUDED	$ -
09 50 00	2X2 ACOUSTIC CEILINGS (WASHABLE)		0	$ 0.00	INCLUDED	$ -
09 50 00	ACOUSTIC CEILINGS	LS	1	$ 30,000	$ 30,000	$ 3.19
09 90 00	FINISH HM DOORS AND HM FRAMES		0	$ 0.00	INCLUDED	$ -
09 90 00	PAINT CMU OR CONCRETE WALLS (INCL BLK FILLER)		0	$ 0.00	INCLUDED	$ -
09 90 00	PAINT DRYWALL WALLS		0	$ 0.00	INCLUDED	$ -
09 90 00	PAINT BOLLARDS		0	$ 0.00	NOT REQ'D	$ -
09 90 00	PAINTING SUBCONTRACTOR ESTIMATE	LS	1	$ 22,500	$ 22,500	$ 2.40
09 90 00	PUNCHLIST		0	$ 0.15	INCLUDED	$ -
01 10 02	FINAL CLEANUP	SF	9,390	$ 0.75	$ 7,043	$ 0.75
	TOTAL FINISHES				**$ 110,105**	**$ 11.73**
13	**SPECIALTIES**					
10 10 00	BACK PAINTED GLASS MARKERBOARDS		0	$ 0.00	BY OWNER	$ -
10 14 00	SIGNAGE PLAQUES AND LETTERING	LS	1	$ 16,369	$ 16,369	$ 1.74
10 14 00	ALUMINUM BUILDING LETTERING (8"H)		0	$ 0.00	INCLUDED	$ -
10 14 00	FIRE RESCUE PLAQUE/EMBLEM (31.5" x 31.5")		0	$ 0.00	INCLUDED	$ -
10 26 00	FRP WALL PROTECTION (JANITOR 118)	LS	1	$ 1,512	$ 1,512	$ 0.16
10 40 00	FEC - FIRE EXTINGUISHERS AND CABINETS (RECESSED)		0	$ 0.00	INCLUDED	$ -
10 40 00	FKC - KITCHEN FIRE EX. AND CABINET (RECESSED)		0	$ 0.00	INCLUDED	$ -
10 40 00	FH - FIRE EXTINGUISHERS ON BRACKETS		0	$ 0.00	INCLUDED	$ -
10 40 00	FE - FIRE EXTINGUISHERS AT EXTRACTOR & STORAGE		0	$ 0.00	NOT REQ'D	$ -
10 40 00	FIRE EXTINGUISHERS	LS	1	$ 1,106	$ 1,106	$ 0.12
10 51 00	WOOD LOCKERS - FURNISHED AND INSTALLED	LS	1	$ 33,820	$ 33,820	$ 3.60
10 21 00	SHOWER STALLS		0	$ 0.00	INCLUDED	$ -
10 21 00	TOILET PARTITIONS		0	$ 0.00	INCLUDED	$ -
10 28 00	TOILET ACCESSORIES MEN'S BATHROOM		0	$ 0.00	INCLUDED	$ -

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
10 28 00	TOILET ACCESSORIES WOMEN'S BATHROOM		0	$ 0.00	INCLUDED	$ -
10 28 00	TOILET ACCESSORIES SMALL TOILETS		0	$ 0.00	INCLUDED	$ -
10 28 00	TOILET PARTITIONS AND ACCESSORIES	LS	1	$ 9,269	$ 9,269	$ 0.99
08 40 10	MIRRORS		0	$ 0.00	INCLUDED	$ -
	TOTAL SPECIALTIES				$ 62,076	$ 6.61
14	**EQUIPMENT AND FURNISHINGS**					
11 21 73	WASHER EXTRACTOR (135LB CAPACITY)			$ 0.00	By Owner	$ -
11 40 00	WASHER - INSTALL ONLY	EA	1	$ 260.50	$ 261	$ 0.03
11 40 00	DRYER - INSTALL ONLY	EA	1	$ 245.00	$ 245	$ 0.03
11 40 00	ICEMAKER - INSTALL ONLY	EA	1	$ 442.00	$ 442	$ 0.05
11 40 00	ELECTRIC RANGE - INSTALL ONLY	EA	2	$ 320.00	$ 640	$ 0.07
11 40 00	REFRIGERATOR/FREEZER - INSTALL ONLY	EA	2	$ 442.00	$ 884	$ 0.09
11 40 00	TELEVISION - INSTALL ONLY	EA	1	$ 279.00	$ 279	$ 0.03
11 40 00	60" RANGE HOOD - FURNISH AND INSTALL (NO FP)		0	$ 0.00	INCLUDED	$ -
12 20 00	MINI BLINDS	LS	1	$ 3,565	$ 3,565	$ 0.38
12 35 31	STAINLESS STEEL OPEN BASE CABINETS - KITCHEN		0	$ 0.00	INCLUDED	$ -
12 35 31	STAINLESS STEEL BASE CABINETS - KITCHEN		0	$ 0.00	INCLUDED	$ -
12 35 31	STAINLESS STEEL ISLAND W/ SS COUNTERTOP		0	$ 0.00	INCLUDED	$ -
12 35 31	STAINLESS STEEL COUNTERTOPS 24" - KITCHEN		0	$ 0.00	INCLUDED	$ -
12 35 31	STAINLESS STEEL COUNTERTOPS 24" - CORRIDOR 114		0	$ 0.00	INCLUDED	$ -
12 35 31	STAINLESS STEEL WALL END CAPS		0	$ 0.00	INCLUDED	$ -
12 35 31	STAINLESS STEEL PACKAGE - BASE CABS, CTOPS	LS	1	$ 75,951	$ 75,951	$ 8.09
	TOTAL EQUIPMENT AND FURNISHINGS				$ 82,267	$ 8.76
15	**SPECIAL CONSTRUCTION**					
	TOTAL SPECIAL CONSTRUCTION				$ -	$ -
16	**VERTICAL TRANSPORTATION**					
	TOTAL VERTICAL TRANSPORTATION				$ -	$ -

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
17	**FIRE SPRINKLER**					
21 00 00	FIRE SPRINKLER SYSTEM	SF	9,390	$ 6.42	$ 60,280	$ 6.42
	TOTAL FIRE SPRINKLER				$ 60,280	$ 6.42
18	**PLUMBING**					
22 00 00	PLUMBING	SF	9,390	$ 15.92	$ 149,500	$ 15.92
22 00 00	TYPE L COPPER WATER PIPING PREMIUM		0	$ 0.00	NOT REQ'D	$ -
22 00 00	UNDERSLAB PLUMBING				INCLUDED	$ -
22 00 00	PLUMBING FIXTURES				INCLUDED	$ -
22 00 00	ELECTRIC WATER COOLER				INCLUDED	$ -
22 00 00	PLUMBING INSULATION				INCLUDED	$ -
22 00 00	FIRE STOPPING AND SAFING				INCLUDED	$ -
22 00 00	OIL INTERCEPTOR				INCLUDED	$ -
22 00 00	LINT TRAP (LAUNDRY)				INCLUDED	$ -
22 00 00	GREASE TRAP (KITCHEN)				INCLUDED	$ -
22 00 00	TRENCH DRAINS (AT EXTRACTOR)		0	$ 0.00	INCLUDED	$ -
	TOTAL PLUMBING				$ 149,500	$ 15.92
19	**HVAC**					
23 00 00	HVAC SYSTEM	SF	9,390	$ 33.62	$ 315,660	$ 33.62
23 00 00	SHEET METAL DUCTWORK				INCLUDED	$ -
23 00 00	GRILLES, REGISTERS, DIFFUSERS				INCLUDED	$ -
23 00 00	TEMPERATURE CONTROLS				INCLUDED	$ -
23 00 00	TEST AND BALANCE				INCLUDED	$ -
23 00 00	KITCHEN HOOD (INCL VENT DUCTS)				INCLUDED	$ -
23 00 00	MAGNEGRIP EXHAUST CAPTURE SYSTEM (HIGH BAY)				INCLUDED	$ -
	TOTAL HVAC				$ 315,660	$ 33.62
20	**ELECTRICAL**					
26 00 00	ELECTRICAL SYSTEMS	SF	9,390	$ 49.65	$ 466,249	$ 49.65
26 00 00	100kW EMERGENCY GENERATOR W/ENCLOSURE				INCLUDED	$ -
26 00 00	GENERATOR LOAD BANK				INCLUDED	$ -
26 00 00	FUEL LEAK DETECTION				INCLUDED	$ -
26 00 00	FUEL FOR GENERATOR (TESTING)				INCLUDED	$ -
26 00 00	FUEL FOR GENERATOR (AFTER TESTING)		1		INCLUDED	$ -
	TOTAL ELECTRICAL				$ 466,249	$ 49.65
21	**LOW VOLTAGE - SECURITY AND LIFESAFETY**					

stellar
TAKING SOLUTIONS FURTHER

STELLAR
DATE: November 5, 2021
PROJECT: COJ FIRE STATION No. 65
PROJ NUM: PROJECT NUMBER

MAIN LEVEL:	9,390
2ND LEVEL:	0
TYP LEVEL:	0
NUM TYP LVLS:	0
GROSS SQ.FT:	9,390
MO	8
WK	35

NEW FIRE STATION BUILDING

SPEC. NO.	DESCRIPTION	UNIT	QUANTITY	UNIT COST	BUDGET	COST/ SQ.FT.
28 00 00	FIRE ALARM				INCLUDED	$ -
27 00 00	COMMUNICATIONS				INCLUDED	$ -
28 00 00	ELECTRONIC SAFETY & SECURITY				INCLUDED	$ -
28 00 00	FIRE STATION ALERTING SYSTEM (FSAS)	ALLOW	1	$ 70,000	$ 70,000	$ 7.45
	TOTAL LOW VOLTAGE - SECURITY AND LIFESAFETY				$ 70,000	$ 7.45

stellar | TAKING SOLUTIONS FURTHER®

Assumptions and Clarifications

© Stellar 2014

stellar

City of Jacksonville
Fire Station 65
Assumptions and Clarifications
November 5, 2021

01 00 00 GENERAL REQUIREMENTS

1. This GMP Budget Estimate is based on 90% Drawings and Specifications dated October 29, 2021.
2. We include a payment and performance bond.
3. We include an allowance of $7,500 for City of Jacksonville plan review and permit fees.
4. We include an allowance of $35,000 for JEA Utility connection fees, meters, impact fees, etc... The final amount will be adjusted up or down via change order to reconcile the actual amount.
5. We include Builders Risk Insurance.
6. We assume temporary utilities' usage fees to be by Owner.
7. We include Florida sales tax.
8. We include sustainable certification through an industry recognized third party such as LEED, Green Globes, or Florida Green Building Coalition.
9. We do accept payments with credit cards. If a credit card is used there will be a 3% fee added to the amount being paid. This additional 3% fee is over and above the contract value.
10. This GMP does not include provisions for a Covid-19 "fully vaccinated" project site.
11. Davis Bacon wages are not included.
12. JSEB participation is currently included at XX%. Participation beyond this rate will require additional cost.

02 00 00 DEMOLITION

1. No demolition is included. It is assumed the site is clear and ready for construction.

03 00 00 CONCRETE

1. We include foundations, slab on grade and structural concrete.
2. All site concrete paving and sidewalks is included.

04 00 00 Masonry

1. Split face CMU with water repellent admixture is included.

05 00 00 STEEL

1. Steel bollards and miscellaneous steel is included.
2. Galvanized gates at dumpster enclosure.
3. Steel brackets at trusses.

06 00 00 ROUGH CARPENTRY & FINISH CARPENTRY

1. We include wood roof trusses and plywood sheathing

stellar

2. Wood blocking as required.
3. Plastic laminate cabinetry is included.
4. Bunker gear storage casework is included.
5. Level 5 Drywall Finishes are not included.

07 00 00 THERMAL AND MOISTURE PROTECTION

1. Architectural asphalt roof shingles as specified.
    a. Two alternate roof shingles are proposed as a ($35,000) savings if Owner would like to use in lieu of specified shingles; they are Owens Corning "TruDefinition Duration" or GAF "Timberline HDZ".
2. Sheet metal gutters and downspouts are included.
3. Spray foam insulation at underside of deck and high walls.
4. Batt insulation included at walls as indicated.
5. Foam insulation infill in CMU walls.

08 00 00 DOORS & WINDOWS

1. Aluminum storefronts and punched windows are included.
2. All glass and glazing is included.
3. Hollow metal frames & doors and wood doors are included.
4. All door hardware is included.
5. Six (6) 14'x14' Non-Insulated sectional overhead doors are included with accessories.

09 00 00 FINISHES

1. All framing, insulation and drywall is included.
2. 2x2 acoustical grid ceiling is included.
3. Ceramic tile floors and walls are included as indicated on plans.
4. Stained and sealed concrete floors are included as indicated on plans.
5. Sheet rubber flooring and 4" resilient base is included as indicated on plans.
6. Paint is included as indicated on plans.

10 00 00 SPECIALTIES

1. Wood lockers are included as indicated on plans.
2. Toilet partitions and specialties as indicated on plans.
3. Fire extinguishers and cabinets as indicated on plans.
4. Signage and building lettering is included.
5. One (1) 25' flagpole is included.

11 00 00 EQUIPMENT

1. Washer Extractor is by owner.
2. Washer & Dryer, icemaker, electric ranges, refrigerators/freezers and television will be provided by Owner and installed by Contractor.
3. Exercise equipment, if any, is furnished and installed by Owner.

stellar

12 00 00 FURNISHINGS

1. We exclude all furniture and office equipment. To be furnished and installed by Owner.
2. Site furniture, if any, is excluded.

13 00 00 SPECIAL CONSTRUCTION

1. N/A

14 00 00 CONVEYING EQUIPMENT

1. N/A

21 00 00 FIRE PROTECTION

1. We include a wet fire sprinkler system for protection of the building.
2. No sprinkler system (wet or dry) is included at the exterior Extractor and Storage Room.
3. We include high wall mounted wet sprinkler system at the Main Entrance and Patio canopies.
4. A Fire Department Connection (FDC) is included.

22 00 00 PLUMBING

1. Plumbing, piping and insulation included as indicated on plans.
2. All plumbing fixtures and water coolers are included.
3. Oil interceptor, lint and grease traps are included.
4. Color coding or painting of exposed plumbing piping is not included.

23 00 00 HVAC

1. HVAC equipment and controls are included.
2. All HVAC ductwork and accessories.
3. All air distribution devices are included.
4. Magnegrip exhaust capture system is included at the high bay to capture vehicle exhaust.
5. A Ductless Split System is included in the base project for the Bunker Gear Room.
   If the owner wishes to eliminate this split system, then the deduct is ($3,875).

26 00 00 ELECTRICAL

1. All electrical gear, panels and equipment are included.
2. All devices, receptacles, conduits, boxes, wiring and accessories.
3. A Fire Alarm system is included.
4. A 100kW Emergency Generator w/enclosure is included.
5. We have included for Bi-Directional Antenna System (BDA) TESTING ONLY. We have NOT INCLUDED for any equipment, installation or labor for a system. This will be determined upon test results if anything is required at all. If required by Fire Officials, we will provide pricing at that time and incorporate into the project via a change order.
6. Site electrical & lighting are included.

stellar

7. Direct bury site light poles & fixtures are included.
8. Voice/Data conduits, cabling, connections are included.
9. Card Readers and conduits to Comms Room for Access Control is included.
10. Access Control equipment is not included.
11. Audio/Visual equipment is not included.
12. Fire Station Alerting System (FSAS) by Purvis: we are carrying an allowance of $70,000 for a complete installed system. At this time the system drawings and specification have not been provided. The A/E is coordinating with PURVIS to complete the design and specifications. The final amount will be adjusted up or down via change order once the drawings and specifications are received and all affected subcontractors can price the work accurately.

31 00 00 EARTHWORK

1. Surveying and layout is included.
2. Traffic control is included.
3. Erosion control is included.
4. Site demolition and clearing & grubbing is included.
5. Retention pond and underdrains are included.
6. Import fill, mass grade and balance site is included.
7. Building pad is included.
8. Stabilization, base and grading required for paving.
9. All asphalt paving is included.
10. All site concrete paving and sidewalks are included.
11. All pavement markings and striping are included.

32 00 00 EXTERIOR IMPROVEMENTS

1. Landscape and irrigation.
2. Trash enclosure and gates are included.
3. Chain link fence & gates are included. Motorized gate is included at driveway.

33 00 00 UTILITIES

1. All site utilities and piping are included.
2. Stormwater structures and piping are included.
3. Sanitary sewer manholes, piping and lift station are included.
4. Domestic water piping, meter box and backflow preventer is included.
5. Fire water piping and hydrant are included.

stellar | TAKING SOLUTIONS FURTHER®

Project Documents

© Stellar 2014

EXHIBIT B

stellar

- Architectural / MEPF / Structural Drawings dated 10.29.2021
- Civil Drawings dated 10.26.2021
- Project Specifications dated 11.1.2021

stellar | TAKING SOLUTIONS FURTHER®

Project Schedule

© Stellar 2014

COJ Fire Station 65
90% GMP Deliverable Schedule

stellar
TAKING SOLUTIONS FURTHER

Activity Name	Original Duration	Start	Finish
COJ Fire Station 65	279	15-Sep-21 A	06-Oct-22
Design	41	15-Sep-21 A	23-Nov-21
COJ/JFRD Review & Comment	9	15-Sep-21 A	15-Oct-21 A
80% Design Deliverable	0		01-Nov-21
90% Design Development	25	28-Sep-21 A	01-Nov-21 A
COJ/JFRD Review & Comment	9	01-Nov-21	11-Nov-21
90% Revised Design Deliverable	8	12-Nov-21	23-Nov-21
90% Design Services Complete	0		23-Nov-21
Permitting	65	01-Nov-21	03-Feb-22
SJRWMD Permitting	35	01-Nov-21	21-Dec-21
COJ Civil Permitting - 10 Set Review	40	08-Nov-21	06-Jan-22
Building Permit Review Cycle 1	20	15-Dec-21	13-Jan-22
Building Permit Review Cycle 2	15	14-Jan-22	03-Feb-22
Permitting Complete	0		03-Feb-22
Preconstruction	103	15-Sep-21 A	10-Feb-22
60% Budget Deliverable	0		15-Sep-21 A
GMP Deliverable	0		01-Nov-21
Approve Early Release Package - Trusses & Truss Engineering	0		01-Nov-21
90% GMP Development	25	28-Sep-21 A	01-Nov-21 A
GMP Approval - Notice to Proceed with Construction	0		12-Nov-21
COJ/JFRD Review & Approval of GMP	10	01-Nov-21	12-Nov-21
Truss Engineering	25	01-Nov-21	07-Dec-21
Truss Production	45	08-Dec-21	10-Feb-22
Construction	175	04-Feb-22	06-Oct-22
Sitework	110	18-Feb-22	21-Jul-22
Pond Excavation	5	18-Feb-22	24-Feb-22
Utilities	20	25-Feb-22	24-Mar-22
Mass Grading	15	25-Mar-22	14-Apr-22
Construct Parking Lots & Entrance Road	40	15-Apr-22	09-Jun-22
Sidewalks & Hardscapes	15	10-Jun-22	30-Jun-22
Landscape & Irrigation	15	01-Jul-22	21-Jul-22
Building	175	04-Feb-22	06-Oct-22
Mobilization	5	04-Feb-22	10-Feb-22
Building Pad	5	11-Feb-22	17-Feb-22
Foundations	10	18-Feb-22	03-Mar-22
Underslab MEP	8	04-Mar-22	15-Mar-22
Masonry Walls & Tilt Beams	30	04-Mar-22	14-Apr-22
Place & Finish Slab on Grade	12	08-Apr-22	25-Apr-22
Erect Roof Trusses & Roof Sheathing	15	26-Apr-22	16-May-22
Interior Framing	8	17-May-22	26-May-22
Roofing	15	10-May-22	30-May-22
Insulation	5	31-May-22	06-Jun-22
Windows & Doors	8	31-May-22	09-Jun-22
MEP Rough In	18	20-May-22	14-Jun-22
Hang & Finish Drywall	13	09-Jun-22	27-Jun-22
Tile Restrooms	10	17-Jun-22	30-Jun-22
Painting	10	28-Jun-22	11-Jul-22
Acoustical Ceilings	13	07-Jul-22	25-Jul-22
Sealed Concrete Floors	10	26-Jul-22	08-Aug-22
Millwork	5	02-Aug-22	08-Aug-22
MEP Trim	18	26-Jul-22	18-Aug-22
Specialties & Toilet Accessories	5	19-Aug-22	25-Aug-22
Punch List & Final Inspections	10	26-Aug-22	08-Sep-22
Substantial Completion	0		08-Sep-22
Owner Training	5	09-Sep-22	15-Sep-22
Commissioning	20	09-Sep-22	06-Oct-22
O&M Manuals / Closeout Documents	20	09-Sep-22	06-Oct-22
Final Completion	0		06-Oct-22

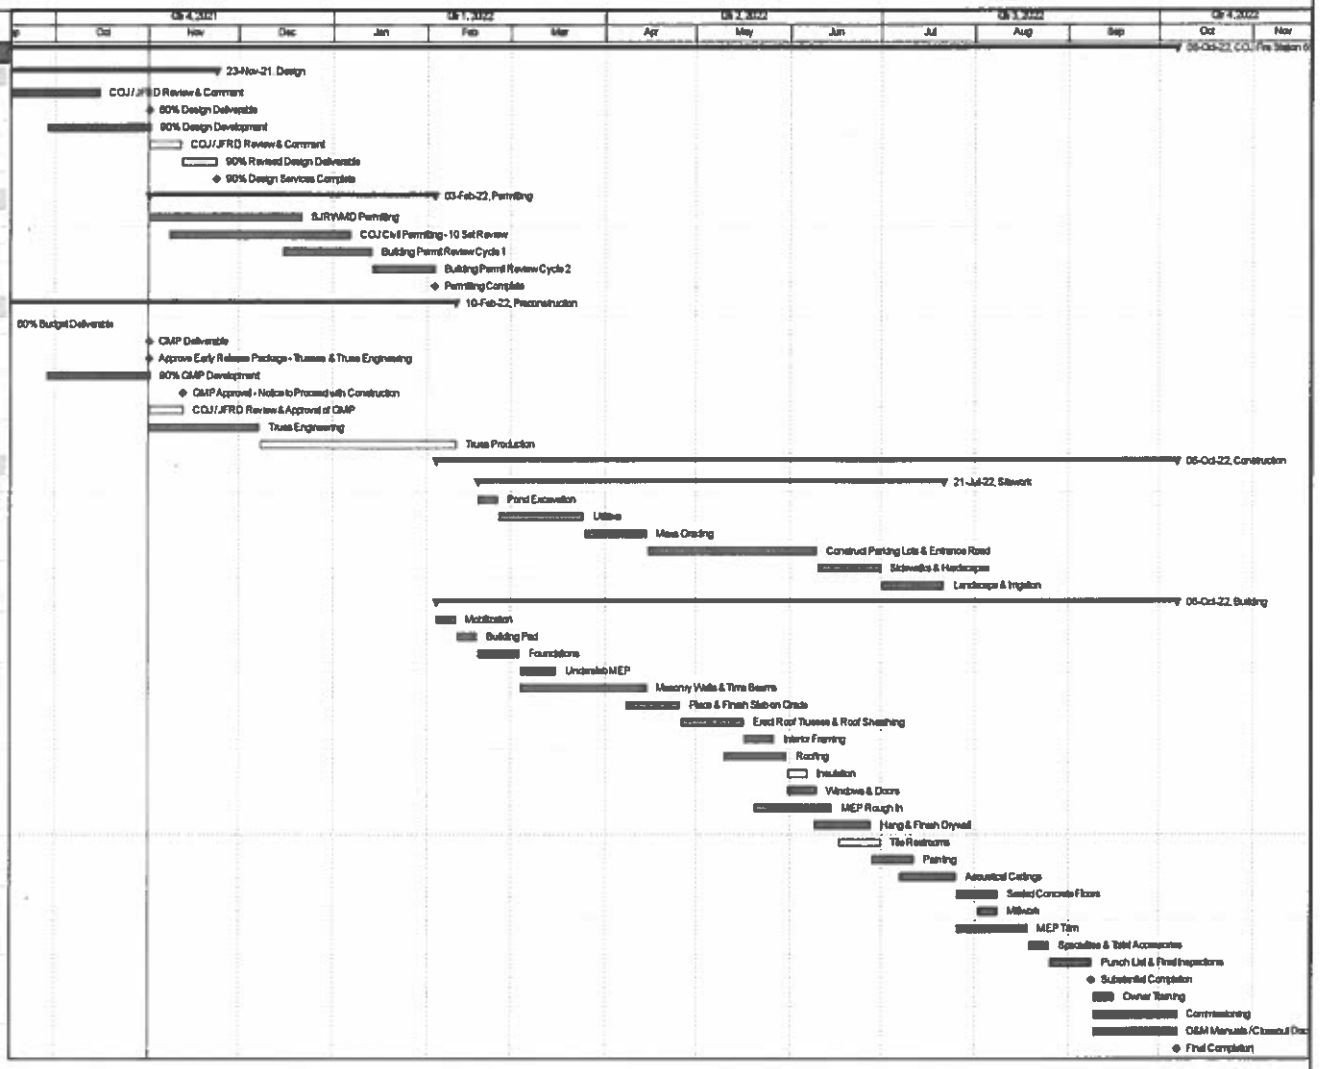

Actual Work
Critical Remaining W...
Remaining Work
Milestone

11/1/21 © Oracle Corporation

EXHIBIT B

stellar | TAKING SOLUTIONS FURTHER®

Supporting Documents

© Stellar 2014

City of Jacksonville: Fire Station 65

Construction Cost Inflation Report

November 1, 2021

Executive Summary

The current construction market volatility has continued to impart inflationary pressures on capital improvement projects. Construction input costs have risen sharply throughout 2020 and 2021 as a result of supply chain interruptions and labor shortages. Stellar has remained committed to working alongside clients to manage project budgets through these unprecedented times. Unfortunately, the majority of the cost increases are occurring at the manufacturer and "producer input" level, where construction managers and design-builders have little control over price volatility. The following summary outlines some of the key inflationary components of the industry and how those price increases are affecting project costs in the northeast Florida region.

In September 2021, the Associated General Contractors (AGC) issued the latest Construction Inflation Alert. This publication tracks construction input inflation and provides a national benchmark of the industry. **The report found that construction input costs have increased 27.8% from April 2020 to August 2021.** The report further identifies the material index for steel products has increased 111% in the same period. Below is a chart from the AGC report that outlines price changes of key building materials over a period of time from April 2020 to August 2021.

FIGURE 2

Price changes for construction and selected materials

April 2020- August 2021

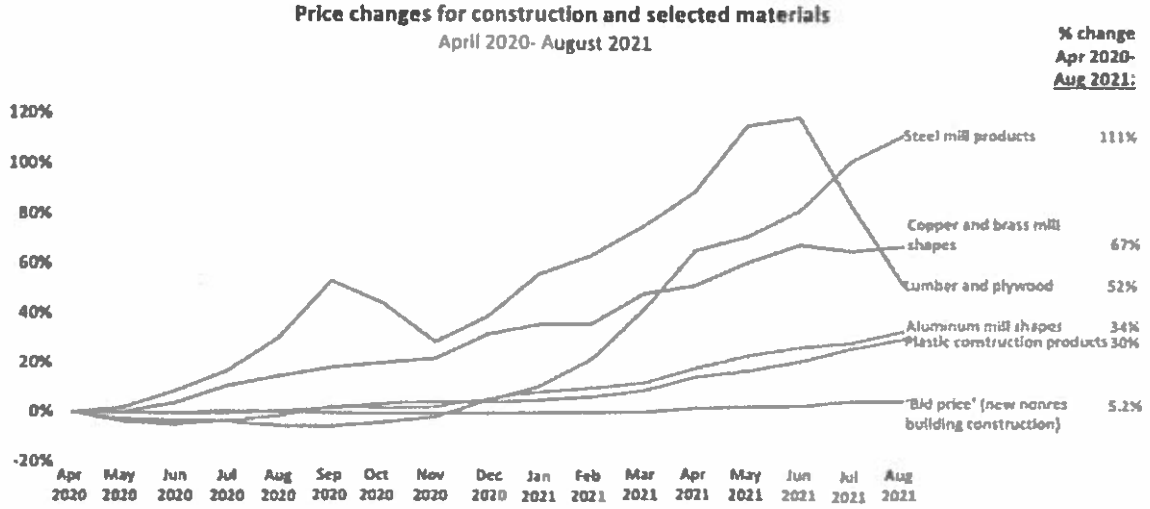

Source: Bureau of Labor Statistics, producer price indexes (PPIs) for new nonresidential building construction (bid prices), gypsum products, wood, metal products, and plastic products, not seasonally adjusted

Source: Associated General Contractors Construction Inflation Alert September 2021

While the supply chain interruptions have created significant price increases in materials, construction trade labor scarcity has also driven up construction costs. The construction industry was already suffering from a declining qualified workforce in the trades, however, post pandemic employment shortages have exacerbated the existing condition. The Employment Cost Index (ECI) which measures employee wages, has posted record breaking year over year increases. In July 2021, the ECI was up 2.9% year over year, which was the single greatest increase since 2018. While wages have grown at a rate much slower than materials, labor is still a contributing factor to the growing inflation within the construction industry.

Fire Station 65 Impact

Stellar has seen these inflationary forces take direct impact on the Fire Station 65 project. Overall, the project costs are elevated beyond the equivalent historical data of years past. Stellar has seen elevated costs throughout most of the building trades, however, commodity driven scopes such as wood trusses, metals, electrical, plumbing, and HVAC continue to trend well above the historical average. These inflated costs are directly attributable to the increased material input costs and the increased costs for high demand skilled labor.

Stellar has taken value management into account throughout the design process, while working to preserve the prototype design. For example, our team has analyzed wood versus light gage metal roof trusses. As seen in the following charts and graphs, the current wood and lumber costs have retreated while metals remain significantly escalated. Therefore, wood trusses proved to be the most cost-effective option.

Copper is a commodity that has been subject to significant inflation. Stellar recommends entertaining the option of utilizing aluminum feeders for higher voltage electrical feeders. This will provide project savings eliminating the amount of copper required.

Supporting Information & Data

In an effort to provide transparency and clarity, Stellar has assembled supporting documentation to substantiate the inflation and volatility on the current construction market. The following data is a combination of material cost indices and industry notifications reflecting said inflation. Stellar has provided snapshots timeline cost information for lumber, metals, rubber/plastics, and asphalt shingles. Each of these index reports show significant increases over the past two years of market volatility.

LUMBER

Nasdaq - Lumber Index (LBS)

FS 63 Lumber Index: 343.7
FS 65 Lumber Index: 707.0
Total Increase: 205.7%

Source: Nasdaq Exchange

STEEL

FS 63 Steel Index: 662.22
FS 65 Steel Index: 1,600.69
Total Increase: 241.72%

Source: NYSE American Steel Index

Rubber & Plastics: Plastic Water Pipe

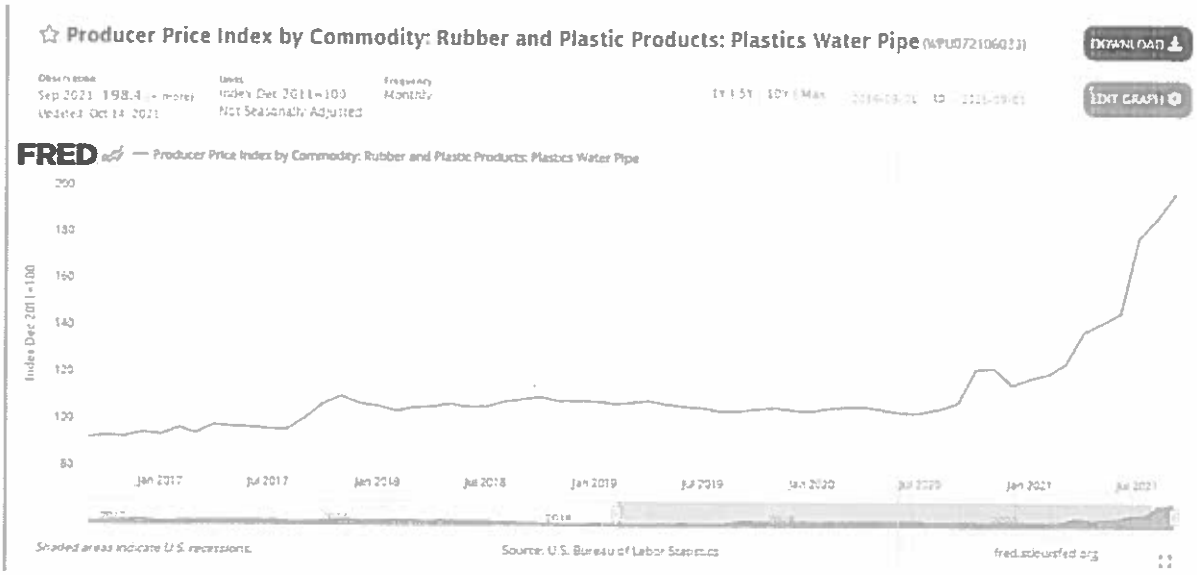

FS 63 Plastic Pipe Index: 108.1
FS 65 Plastic Pipe Index: 198.4
Total Increase: 183.53%

Asphalt Shingles

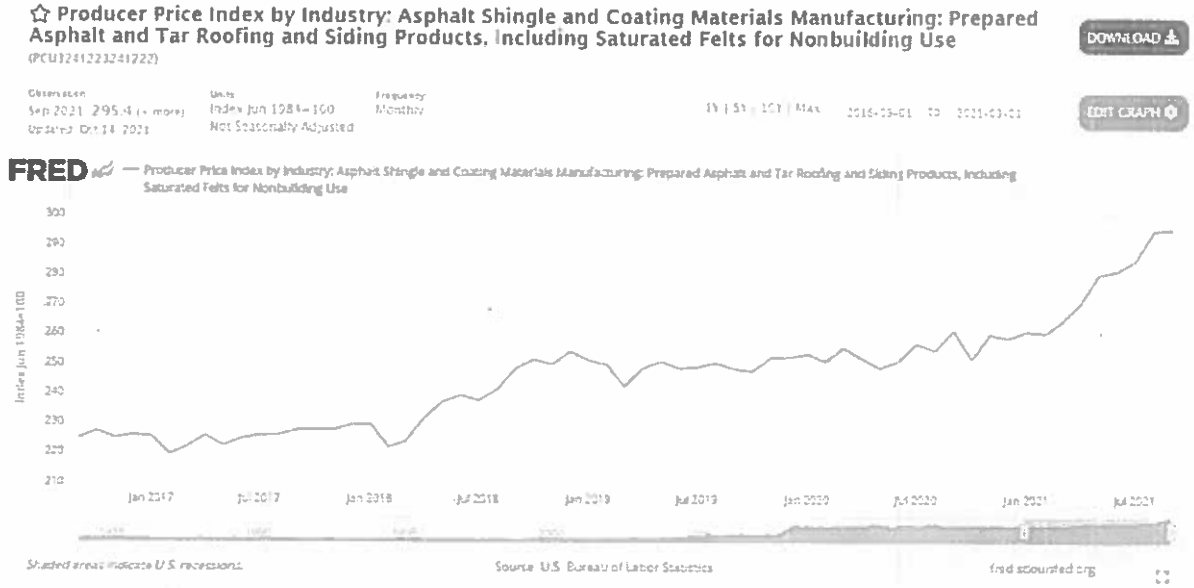

FS 63 Asphalt Shingle Index: 248.5
FS 65 Asphalt Shingle Index: 295.4
Total Increase: 19%

Source: FRED Economic Data

EXHIBIT B

Supplier/Vendor Increase Notifications:

December 28th, 2020

Additional Price Increase Announcements

To Our Valued Customers:

Due to continued increase announcements from domestic steel mills, ClarkDietrich will implement two minimum price increases of 10% on all products for all markets effective:

- **February 1st, 2021**
- **March 1st, 2021**

These increase announcements are in addition to our January 4th, 2021 increase announcement.

ClarkDietrich will continue to honor all existing quotes in accordance with our current job quote policy. As a reminder, job quotes that are not committed within 30 days after issuance are invalid and will be requoted to reflect new price levels upon request. A copy of our policy can be found on our website at: www.clarkdietrich.com/support-tools/sales-forms.

New price sheets reflecting these increases will be distributed prior to the increase date. If you have any questions, please contact your local Sales Representative.

Thank you for your continued support.

Sincerely,

ClarkDietrich

EXHIBIT B

ClarkDietrich.

October 29, 2020

Price Increase Announcement

To Our Valued Customers:

Due to additional increase announcements from domestic steel mills, ClarkDietrich will implement a minimum price increase of 10% on all products for all markets effective November 30, 2020. This increase is in addition to our November announcement effective 11/1/20.

ClarkDietrich will continue to honor all existing quotes in accordance with our current job quote policy. As a reminder, job quotes that are not committed within 30 days after issuance are invalid and will be requoted to reflect new price levels upon request. A copy of our policy can be found on our website at: www.clarkdietrich.com/support-tools/sales-forms.

New price sheets reflecting this increase will be distributed by mid November 2020. If you have any questions, please contact your local Sales Representative.

Thank you for your continued support.

Sincerely,

ClarkDietrich

EXHIBIT B

Kathy Aldridge

From: Rhonda Dunn <rhonda@wilkinsonsteelsupply.com>
Sent: Monday, January 11, 2021 3:22 PM
Subject: Mill Pricing

Good afternoon.

Oh my goodness, another mill price increase!

On January 8, 2021, the mills announced another immediate price increase of $50.00 per ton on all rebar. This brings the total mill increases to $175.00 per ton since November 15, 2020. We will do our best to hold down prices.

Thanks,

Dann E. Dunn

Wilkinson Steel Supply, LLC
3210 Faye Rd.
Jacksonville, FL 32226
904-757-1522

EXHIBIT B

Oldcastle BuildingEnvelope
A CRH COMPANY

September 29, 2021

RE: Architectural Glass Price Increase

To Our Valued Customers:

We continue to provide you the best service and quality in the industry. We are committed to our vision of being the value-added supplier.

Recently, we have received notice from our flat glass manufacturers that pricing will increase up to 12% effective October of 2021. This is the third flat glass raw material increase received in less than one year which is unprecedented. We have continued to see inflation in other raw materials like insulating, laminating, fabrication, and packaging supplies.

In response to these raw material inflationary pressures and rising cost of labor, we find it necessary to increase our selling price on glass products as outlined below:

- 12% ≤6mm Thin Clear Monolithic Glass Products
- 10% ≥8mm Heavy Clear Monolithic Glass Products
- 10% All Other Monolithic Glass Products
- 10% Insulating and Laminated Glass Products
- 10% All Other Products/Services

These prices will be effective with orders placed on October 11th, 2021. Please contact your Sales Representative to confirm and secure current estimates.

We appreciate your business and thank you for your continued support.

Sincerely,

Vishal Singh

Vishal Singh
President, Architectural Glass

5025 LBJ Freeway • Suite 1350 • Dallas, Texas 75244 • www.cbe.com • Phone (214) 273-3400 • Fax (214) 273-3401

EXHIBIT B

Ferguson Waterworks
801 Thorpe Rd.
Orlando, FL 32824

Dear Valued Customer,

Let me begin with a sincere "Thank You" for your continued support as we worked together successfully through one of the most interesting years in recent memory. Of all the lessons and reminders 2020 afforded, perhaps the most significant was the fact that most things are out of our control. Fortunately, we can always choose how we respond. It is in this spirit that we are reaching out today. As trusted advisors we strive to deliver the very best overall experience to the waterworks industry. An important component is providing the latest information to aid our customers in making the best choices for their business.

In the last 30 days we have received price increase notifications from virtually every manufacturer in the industry. There are a variety of factors listed by our vendor partners in the accompanying pages. All point to a sizeable shift in the global supply and demand equation. We welcome the opportunity to discuss with you in the coming weeks. Our sales and leadership teams are looking forward to working with you towards another successful year in 2021.

Thank you again for your partnership and your support of Ferguson Waterworks.

Respectfully,

Darren Campbell

Darren Campbell
General Manager – Central & North FL Waterworks Division

FERGUSON
WATERWORKS

EXHIBIT B

JM Eagle

DELIVERING GOOD WATER TO YOU

Neal Gordon
VP, Waterworks Sales
Phone: 800-621-4404 x 7401
Fax: 310-451-4170
E-mail: nealgordon@jmeagle.com

Sarfaraz Siddiqui
Asst. Manager, Waterworks Sales
Phone: 800-621-4404 X 7905
Fax: 1-800-451-4170
E-mail: safarazsiddiqui@jmeagle.com

JM Eagle
5200 West Century Blvd
Los Angeles, CA 90045

www.jmeagle.com

January 6, 2021

PVC Price Increase — February 1, 2021

Dear Valued JM Eagle Partner,

Following up on our last letter of December 17th, resin costs continue to rise and the global resin supply for the entire PVC market remains very limited.

Westlake, Shintech and Formosa have all announced a +$0.03/lb. price increase to take effect February 1, 2021. This increase comes on top of their +$0.04/lb. increase which took effect January 1st, 2021. In total, that's a +$0.07/lb. increase in only two months.

All resin suppliers report that the PVC resin supply will remain tight due to increasing export demand. This limited supply of raw materials will directly impact the entire PVC pipe market.

With this in mind, we are announcing that **all PVC product pricing will increase effective February 1, 2021.**

For PVC waterworks products specifically:

Immediate Ship
Standard Term

Increased pricing for PVC will apply to all new and expired quotes. JM Eagle will honor all valid quotations at their current prices, subject to availability. We ask all customers to be mindful of terms quoted and to expect further increases.

We will continue to monitor raw material costs and other industry conditions to determine if further actions are necessary.

Thank you for your understanding and cooperation. Best wishes for a happy and a healthy 2021 ahead.

Best Regards,

Neal Gordon
VP, Waterworks Sales

Sarfaraz Siddiqui
Assist. Manager, Waterworks Sales

EXHIBIT B

DELIVERING GOOD WATER TO YOU

Neal Gordon
VP, Waterworks Sales
Phone: 800-621-4404 x 7401
Fax: 310-451-4170
E-mail: nealgordon@jmeagle.com

Sarfaraz Siddiqui
Asst. Manager, Waterworks Sales
Phone: 800-621-4404 X 7905
Fax: 1-800-451-4170
E-mail: safarazsiddiqui@jmeagle.com

JM Eagle
5200 West Century Blvd
Los Angeles, CA 90045

www.jmeagle.com

December 17, 2020

PVC Price Increase — January 1, 2021

Dear Valued JM Eagle Partner,

Following up on our last letter of November 23rd, resin costs continue to rise and the resin supply for the entire PVC market remains very limited.

Westlake and Formosa have today announced a +$0.04/lb. price increase to take effect January 1, 2021. Other resin suppliers are expected to follow shortly. This is in addition to the +$0.03/lb. increase that was announced for December.

In total, PVC resin suppliers have increased pricing +$0.28/lb. the second half of 2020. That is the equivalent of a price increase of 56 blocks!

PVC resin supply remains tight as Westlake is still under Force Majeure conditions. Other resin suppliers are allocating resin accordingly. International demand upon domestic resin manufacturers is anticipated to increase dramatically in 2021.

This scarcity of raw materials will directly impact the entire PVC pipe market.

With this in mind, we are announcing that **all PVC products pricing will increase effective January 1, 2021.**

For PVC waterworks products specifically:

Immediate Ship
Standard Term

Increased pricing for PVC will apply to all new and expired quotes. JM Eagle will honor all valid quotations at their current prices, subject to availability. We ask all customers to be mindful of terms quoted and to expect further increases.

We will continue to monitor raw material costs and other industry conditions to determine if further actions are necessary.

Thank you for your understanding and cooperation. Best wishes for a happy and safe holiday season ahead.

Best Regards,

Neal Gordon
VP, Waterworks Sales

Sarfaraz Siddiqui
Assist. Manager, Waterworks Sales

EXHIBIT B

NAPCO, a Westlake company
2801 Post Oak Blvd., Suite 600, Houston, Texas 77056
Tel: 713.840.7473, Fax: 713.552.0087

Date: January 5th, 2021

To: All Municipal Customers

From: Brent Wetmore,Vice President - Sales

Subject: PVC Pipe Prices – Municipal Products

As we begin 2021 the resin market continues to be volatile as global demand remains strong. The result has been further increases announced for both January and Feb. We are monitoring the prices closely and as a result of these current increases are revising our PVC pipe prices, effective immediately, to the following:

Effective immediately, we are implementing the following PVC Pipe Price:

Immediate Shipments
(immediate release subject to availability)

Standard Quotations

All current orders and quotes will be honored within terms and are subject to our ability to ship. Orders and quotes with expired terms will be re-priced.

If you have any questions regarding product availability or this price increase, please contact your local North American Pipe sales representative.

We appreciate your business and look forward to continuing to serve your PVC pipe needs.

EXHIBIT B

NATIONAL PIPE & PLASTICS, INC.
American-made products since 1970

Corporate Offices
New York Plant
3421 Old Vestal Road, Vestal, NY 13850
800.836.4350 607.729.9381 Fax: 607.729.6130

National Pipe & Plastics, Inc.

Memorandum

Date: December 31, 2020

To: All Sales Representatives

From: Matt Siegel, Pete Craner, Jeff Kurkoski

Subject: Municipal Price Increase

In light of the current state of the PVC pipe industry, effective **January 1, 2021,** we are implementing the following pricing on our municipal products:

Immediate
Standard Quotes

Please note that this supersedes all previous price announcements.

All expired orders and quotes will be repriced at current levels.

Note: Full bundle quantities will be required on all stock and direct shipped orders.

EXHIBIT B

DIAMOND PLASTICS®
CORPORATION
Corporate Headquarters: 1212 Johnstown Rd. • P.O. Box 1608 • Grand Island, NE 68802-1608
800-PVC-PIPE • 800/782-7473 • www.dpcpipe.com

December 30, 2020

TO: Diamond Plastics' Utility Customers

FROM: D. Bauer & S. Yentes

SUBJECT: **Price Increase**

Resin costs continue to rise and the resin supply remains very limited. The additional demand plus reduced production have led to a substantial reduction of resin inventory on hand. Some resin suppliers have announced price increases effective January 1, 2021 with others expected to follow.

We hereby announce the following PVC pipe price increases for standard block items **effective January 1, 2021**.

Immediate Ship:
Standard Quote Terms:

These increases will apply to new and expired quotes.

We hope you, your family and associates are safe and well and wish you a very Happy New Year!

Celebrating Over 30 Years of Excellence

EXHIBIT B

TUBI USA, Inc.
3838 Oak Lawn Ave, Suite 1000
Dallas, TX 75219
M 214-490-4980
T 469-317-6300

January 11, 2021

RE: January 2021 PE Pipe Price Increase

Dear Polyethylene Pipe Customer,

Over the last 10 months we have seen unprecedented and horrific changes in our world due to the global covid-19 pandemic.

While many businesses have seen great profits, most have been left to struggle for financial survival or have had to file for bankruptcy. In 2020, we saw demand for PE pressure pipe fall by over 25% as per the latest Plastics Pipe Institute statistics. PE Pipe manufacturers are among those businesses that have struggled to survive because of capital project delays and increased PE resin costs due to the covid-19 pandemic.

TUBI USA, Inc. worked hard in 2020 to lower our manufacturing costs, however, considering so many resin price increases beginning in June 2020, we can no longer hold prices firm. Attached you will see the letters from our resin suppliers announcing these price increases. Everyone of these price increases have now been implemented. Never have we seen resin increases escalate by 24 cents per pound in such a short period of time from June to December 2020. Even now, we face further increases with every resin manufacturer now announcing another 6 cpp resin price increase for January 2021.

The resin price increases are based on extremely tight resin supply due to:

- Strong domestic and export demand for polyethylene food, medical, and other consumable product packaging
- Rising feedstock costs for ethylene, ethane, and crude oil
- Force Majeure events from resin suppliers Formosa and shutdowns by Braskem in Mexico
- Upcoming maintenance turnarounds by multiple large resin suppliers

As a result, TUBI USA, INC. must increase our prices effective immediately. We greatly appreciate your business and confidence you have placed in us a supplier of your polyethylene pipe needs. If you have any questions regarding this price increase, please reach out to our Sales Manager, Jeff Sevario, or me.

Best Regards,

WL Plastics Corp EXHIBIT B
3575 Lone Star Circle
Suite 300
Fort Worth, TX 76177

Email: jcottle@wlplastics.com
Phone: 281-236-3291

Market Update

January 12, 2020

Dear Valued Customer,

WL Plastics wanted to update you on market conditions that will affect polyethylene pipe pricing. A $ /lb HDPE increase was implemented on December 1, 2020. This increase was driven by a North American HDPE producer, capable of 1.7 billion lbs of annual capacity, shut down with no timeline for re-starting. That manufacturer has not restored HDPE production at this time, keeping HDPE availability at a minimum. Additionally, Ethylene feedstock prices have risen 42% compared to last month. It is evident that the $ /lb January HDPE price increase will be implemented this month. This January HDPE price increase will affect HDPE pipe pricing.

WL Plastics will honor any existing agreements and any valid quotations through the quotation validity date. Any new quotations provided by WL Plastics will reflect these raw material increases.

We greatly appreciate your partnership and continued business. WL Plastics is monitoring the market conditions closely and will communicate changes as they occur so that you may best plan for your business needs. Please feel free to contact me or your WL Plastics Sales Representative with any questions. Thank you.

Regards,

Joshua Cottle

VP of Sales & Marketing

EXHIBIT B

AMERICAN

DUCTILE IRON PIPE

THE RIGHT WAY

January 15, 2021

To: AMERICAN Ductile Iron Pipe Customers and Distributors

Subject: February 15, 2021 Price Increase Announcement

As you may already be aware, raw material costs (scrap) have significantly increased during the last several months. While we have been able to absorb several of those increases, recent rapid escalation of raw material costs has forced us into a position where we can no longer avoid raising our DIP prices. Effective February 15, 2021, we are implementing an increase to all our ductile iron pipe products. This price increase will be directly applicable to our current pricing portal levels which became effective on October 1, 2020.

The increase will be effective for all quotations with bid or submission dates of February 15, 2021 and beyond. Pricing portal quotations which are produced prior to February 15th with bid dates on or after February 15th must be repriced to match February 15th pricing. Portal pricing will be your invoice prices (based on full truckloads), and no orders will be accepted at pricing below quoted prices.

Quotation and shipping terms will remain unchanged. Portal price quotations are only good for up to 60 days from the date of the portal inquiry, and those expiration dates will be listed on all quote footers. All orders will require a pricing portal reference number (ID) and must be within quotation and shipment validity dates. No orders will be accepted without a portal ID number. All orders must be shipped within 90 days or be either repriced or cancelled.

Our sales personnel will work closely with you to ensure that all outstanding quotations and existing orders are managed within the terms stated both in this letter and on all quotation footers.

Additionally, please be aware of the following:

- For specialty products which are made-to-order only (e.g., unique linings/coatings, river crossing pipe, earthquake resistant pipe), we require unrestricted release for shipment as soon as those products become available.
- Any additional handling, re-processing, and/or freight costs incurred as a result of shipment delays will also be charged.
- Future price adjustments to our finished products may be necessary.
- Price adjustment strategies may include escalators or surcharges.
- We may not be able to provide advanced notice of a price adjustment.
- Market conditions may dictate that the quoting and shipment terms stated in this letter are substantially reduced/limited in the future.
- Outstanding quotes and stock orders which are beyond stated terms will be cancelled.

We at AMERICAN appreciate your support, and we thank you for your business.

Sincerely,

EXHIBIT B

US PIPE
FABRICATION
A Forterra Company

109 5th Street
Orlando, FL 32824

October 1, 2020

To: Valued Distribution Partners and Customers
Re: List Price Increase for Ductile Iron Fabricated Pipe effective 12/1/2020

The cost of ductile iron pipe has gone up throughout the year, and will continue, per U.S. Pipe's previously announced October 1 price increase. Labor and other costs have also continued to rise. To cover these costs, U.S. Pipe Fabrication will implement a **List Price increase of 6%** on all Ductile Iron Fabricated Pipe products **effective December 1, 2020**. New list prices will be available on our website on November 1, 2020.

This increase will affect your list prices, but all discounts will remain the same. Quotes will be honored per the terms listed on the quotation. All sales are subject to our Standard Terms and Conditions. Payments are due as stated on your invoice.

We appreciate your continued support, partnership, and understanding as we look forward to a mutually prosperous future. Our Sales and Customer Service teams will be in touch to answer any questions you may have, and please do not hesitate to contact either of us at our phone numbers below if we can be of any assistance.

Best Regards,

Dave Woollums
Vice President U.S. Pipe Fabrication
423-802-8249

Howard Smith
Sr. Vice President of Marketing & Sales
919-757-5411

EXHIBIT B

CUSTOM PIPE & FABRICATION INC.

December 2, 2020

To: Our Valued Customers

Subject: New List Prices / Increase

With the costs associated with the fabrication of ductile iron spools continuing to rise, Custom Pipe & Fabrication will be implementing a new list price catalog for 2021.

List prices will be made available on December 29th and will go into effect on January 4th, 2021. Outstanding quotes will be considered on a case by case basis. Please reach out to your area representative for your multiplier and freight terms.

We greatly appreciate your support and valued business and wish you success in the coming year.

Sincerely,

Michael T. Litty

Vice President - Waterworks

EXHIBIT B

AMERICAN
FLOW CONTROL
THE RIGHT WAY

AFC Price Increase Effective December 14, 2020

Due to increased transportation and material costs, AMERICAN Flow Control will implement a price increase effective December 14, 2020. We will increase prices by reducing discounts applied to our price list dated August 1, 2019. Approximate increases to each product are shown below.

PRODUCT	APPROXIMATE INCREASE
AWWA & UL/FM DRY BARREL FIRE HYDRANTS	
CAPTIVATER® - LOCKING HYDRANT NOZZLE CAP	
2" – 12" RESILIENT WEDGE GATE & TAPPING VALVES	
14" – 24" RESILIENT WEDGE GATE & TAPPING VALVES	
ALPHA™ JOINT ENDS ADDER	
ALL CHECK VALVES	
UL/FM INDICATOR POSTS	
ALL TAPPING SLEEVES	
TRENCH ADAPTER & RETROFIT VALVE BOX INSERT	
ALL REPAIR PARTS	
FIRE HYDRANT EXTENSIONS & TRAFFIC KITS	

Current pricing will be honored on orders without shipping restrictions received on or before December 13, 2020. **There will be no extended shipments, and all material will be shipped as it becomes available.**

We will protect the prices of all documented municipal fixed price contracts through the contract duration provided AMERICAN receives a list of such contracts prior to December 13, 2020. **We will not protect prices on outstanding contractor quotations after the price increase date.**

Thank you for your business. Your AMERICAN Sales Representative will be in contact with you to establish your new discounts as well as answer any questions you may have.

Regards,
Robert H. Patton
Director of Project Management

EXHIBIT B

MUELLER

Mueller Water Products
Headquarters
1200 Abernathy Road NE
Suite 1200
Atlanta, GA 30328

phone: 770-206-4200

November 9, 2020

To: Mueller, US Pipe AWWA and UL/FM PRODUCT DISTRIBUTORS

Re: Price Increase Applying to All AWWA and UL/FM Products

In order to offset continued rising manufacturing costs, we are announcing a price increase for the iron products listed below. This price increase will be effective Monday, December 14, 2020, and will be implemented as indicated below.

AWWA and UL/FM Iron Products:

- Dry Barrel Fire Hydrants
- 2-12" Resilient Wedge Gate and Tapping Valves
- 14" and above - Resilient Wedge Gate and Tapping Valves
- Double Disc Gate and Tapping Valves
- Iron Tapping & Split Repair Sleeves, & Crosses
- Cut-In Sleeves and Valves
- Hydrant Extension and Repair Kits
- Repair Parts for Iron Products
- Indicator Posts

The price change will be implemented as follows:

1. Any orders received before December 14, 2020 with no shipping restrictions will be price protected.
2. Any orders received before December 14, 2020 with customer restricted extended shipping dates will be invoiced at the new price.
3. Material covered in fixed price municipal contracts will be honored for the original contract bid quantities for the duration of the contract.
4. Distributor quotes to contractors will not be price protected. All contractor quoted projects must be ordered before December 14, 2020.

Your Sales Representative will be in contact with you prior to the effective date to review these increases and to answer any questions you may have.

Mike Lindgren

Vice President - Distribution

EXHIBIT B

The Ford Meter Box Company, Inc.

775 Manchester Avenue • P.O. Box 443, Wabash, Indiana U.S.A. 46992-0433
Phone: 260-563-3171 • Fax: 800-826-3487 • Overseas Fax: 260-563-0167 • www.fordmeterbox.com

January 15, 2021

To Our Valued Customers,

Due to escalating raw material and transportation costs, we find it necessary to increase our prices.

Prices for no-lead brass, brass saddles, plastic pit setters, iron meter boxes, covers and lids, drilling machines, and meter testing equipment will increase by . Uni-Flange® joint restraints will increase by . These changes will be implemented by a list price adjustment and will become effective on Friday, February 19, 2021.

All orders received on or after February 19, 2021, will be subject to the new prices. All existing fixed price quotations and special price programs will be honored through the contract period. New quotations may be requested; however, they will be subject to the new prices.

The new price book will be available from our website, www.fordmeterbox.com, on February 12. An Excel price book will be available to customers for downloading on the Ford Meter Box® Distributor Portal. Please contact your Ford® Customer Service Manager to be set up on the portal.

Additionally, price increases from suppliers are impacting the manufacturing costs of our pipeline products (clamps, couplings, tapping sleeves, iron and stainless steel saddles, and fabricated steel products). Ford Meter Box's policy has always been to increase prices only when economically warranted. Regrettably, we anticipate a future price increase on these products and will provide as much advance notice as possible.

Best Regards,

Thomas A. Lower
Vice President
Senior Manager of Sales and Marketing

Rodney A. Kelsheimer
Manager of Inside Sales

EXHIBIT B

SIGMA.
Quality – Service – Commitment – Delivered.

700 Goldman Drive
Cream Ridge, NJ 08514

P: (256) 496-3388
gf1@sigmaco.com

December 28, 2020

To: SIGMA Customers in USA:

Re: Price Announcement for Import AWWA Fittings and MJ Accessories

As detailed in our letter dated December 16, 2020 applicable to import Pipe Restraint Products, SIGMA is absorbing significant cost increases with our imported product driven by the devaluation of the US dollar and increases in raw materials, inland and ocean freight. In particular, the cost of pig iron, foundry coke and other raw materials remains volatile with weekly increases driven by worldwide demand. While we have no certain insight into the future, SIGMA believes these increases will continue well into 2021.

Therefore, SIGMA is announcing a price increase on AWWA MJ, Push-On and Flange Fittings and MJ Accessories. This increase will also be applicable to Fittings with specialty linings and coatings including P-401 lined Fittings and Zinc and FBE coated Fittings.

This price increase will include new List Prices for import AWWA MJ, Push-On and Flange Fittings. For Fittings of 16" or smaller diameter, the List Price increase will be . For Fittings with diameters larger than 16", the List Price increase will be . Also, SIGMA will publish new List Prices for MJ Accessories with an approximate increase of . The new List Prices will be available on SIGMA's website, www.sigmaco.com, by Monday, January 11, 2021.

The effective date will be Monday, February 1, 2021.

In addition, SIGMA is announcing a multiplier reset against these new Price Lists to our previously published multipliers announced in market letters dated January 16, 2020. In many markets, this pricing has declined over the course of this year. With this letter, SIGMA is confirming those published multipliers in the marketplace.

Please contact your SIGMA Territory Sales Manager for confirmation of the published multipliers or with any other questions that you may have.

Finally, we at SIGMA wish you a happy, healthy, and prosperous New Year.

Sincerely,

Greg Fox | VP of Sales
SIGMA Corporation
256.496.3388
GF1@sigmaco.com

PREMIUM SERVICE AND QUALITY 35 YEARS SIGMA

EXHIBIT B

SIGMA.
Quality – Service – Commitment – Delivered.

700 Goldman Drive
Cream Ridge, NJ 08514

P: (256) 496-3388
gf1@sigmaco.com

December 16, 2020

To: SIGMA Customers in USA:

Re: Price Announcement for Import Pipe Restraint

At the outset, we at SIGMA wish you and your family a peaceful and joyful holiday season even as we continue to be both concerned and cautious about the ongoing pandemic. With successful vaccines already in the process of distribution, we look forward to a gradual return to normalcy in 2021.

Meanwhile, the COVID-19 pandemic has affected some of our supply chain operations and increased our costs. Shipping companies have curtailed their vessel operations and hence available container space all while the overall demand remains strong. The result is increased ocean freight costs. In addition, the US dollar has weakened against currencies in other countries particularly those countries in Asia. Altogether, SIGMA is absorbing meaningful increases with cost of goods due to the combined impact of COVID-19 disruptions, US dollar devaluation and increased costs of raw materials, ocean and inland transportation, domestic labor and healthcare.

Therefore, SIGMA is announcing new List Prices for import Pipe Restraint Products. These new List Prices will be higher than our current List Prices. These List Prices will be available on SIGMA's web site, www.sigmaco.com, by Monday, December 28th.

The effective date will be Monday, January 11, 2021.

In addition, SIGMA is announcing a multiplier reset against these new lists to our previously published multipliers announced in market letters dated January 15, 2020. In many markets, this pricing has declined over the course of this year. With this letter, SIGMA is confirming those published multipliers in the marketplace.

Please contact your SIGMA Territory Sales Manager for confirmation of the published multipliers or with any other questions that you may have.

All of us at SIGMA thank you for your business and support in this most unusual year.

Sincerely,

Greg Fox | VP of Sales
SIGMA Corporation
256.496.3388
GF1@sigmaco.com

PREMIUM SERVICE AND QUALITY 35 YEARS SIGMA

EXHIBIT B

SIGMA
Quality – Service – Commitment – Delivered.

700 Goldman Drive
Cream Ridge, NJ 08514

P: (256) 496-3388
gf1@sigmaco.com

January 4, 2021

To: SIGMA Customers in USA:

Re: Price Announcement for Domestic AWWA Fittings and MJ Accessories

SIGMA is announcing new List Prices for domestic AWWA Fittings and MJ Accessories. These new List Prices will be approximately higher than our current published List Prices.

These new List Prices will be published on SIGMA's website, www.sigmaco.com, by Monday, January 18, 2021.

The effective date will be Monday, February 1, 2021.

Applicable multipliers have been previously published. For confirmation, please contact your SIGMA Territory Sales Manager.

We at SIGMA appreciate both your business and support.

Sincerely,

Greg Fox | VP of Sales
SIGMA Corporation
256.496.3388
GF1@sigmaco.com

PREMIUM SERVICE AND QUALITY 35 YEARS SIGMA

EXHIBIT B

January 15, 2021

To: Our Valued Customers

RE: **Domestic Joint Restraint Multiplier Increase**

We are experiencing substantial cost increases in raw materials, transportation, and other associated costs of manufacturing; therefore, we are increasing our Domestic Joint Restraint multipliers approximately for use with our current Price List, effective February 1, 2021.

The current Domestic Joint Restraint Price List, labeled DOM-JRPL.14.01B, is posted and available on our website at www.StarPipeProducts.com.

Prior committed pricing on 2020 Municipal and Annual Contracts will be honored per our original agreements. All orders received before January 31, 2021, will be price protected for immediate shipment only. We remain committed to earning your business. Thank you for your continued support. We wish you a Happy, Healthy & Safe 2021!

Sincerely,

Jason O'Nan

Jason O'Nan, Vice President
Star® Pipe Products

STAR® PIPE PRODUCTS
4018 WESTHOLLOW PARKWAY HOUSTON, TEXAS 77082-4604
wwww.starpipeproducts.com
T: 281.558.3000
F: 281.558.9000

EXHIBIT B

December 21, 2020

To: Our Valued U.S. Customers

RE: EFFECTIVE February 1st, 2021 – List Price Increase for Import Joint Restraints and Updated Multipliers

Due to continued cost increases in raw materials and transportation costs, we are announcing a List Price increase for our Import Joint Restraint Products, effective Monday, February 1, 2021. The Excel format with the new list prices is attached to this email. We will also post it on our website at www.StarPipeProducts.com. The PDF version will follow shortly.

In addition, the associated multiplier for our Waterworks stocking distributors for the new Import Joint Restraint Products price list is .

IMPORT PRODUCTS	MULTIPLIER	PRICE LIST VERSION
Joint Restraint Products	0.	IMP-JRPL.21.01

Prior committed pricing on 2020 Municipal and Annual Contracts will be honored per our original agreement. All joint restraint orders received before January 31st, 2021, will be price protected for immediate shipment only. We remain committed to earning your business. Thank you for your continued support.

Merry Christmas & Happy Holidays!

Sincerely,

Jason O'Nan

Jason O'Nan, Vice President
Star® Pipe Products

STAR® PIPE PRODUCTS
4018 WESTHOLLOW PARKWAY HOUSTON, TEXAS 77082-4604
wwww.starpipeproducts.com
T: 281.558.3000
F: 281.558.9000

TÜVRheinland

FOUNDRY

EXHIBIT B

STAR PIPE PRODUCTS

January 5, 2021

To: Our Valued Star Pipe Customers in:

AL, AR, FL, GA, KS, LA, Western MO, MS, NC, OK, SC, TN & TX

RE: Multiplier Increases for Import & Domestic Fittings, Accessories and Municipal Castings Net Price Increase

Effective Monday, February 1, 2021, please use the multipliers with the respective price lists below. All price lists will be posted on our website at www.StarPipeProducts.com on or before January 15, 2021.

Import Products	Multipliers	Price Lists
Utility Fittings		IMP-UPL.21.01
FBE Fittings		IMP-FBE-UPL.21.01
P401 Fittings		IMP-P401-UPL.21.01
Zinc Fittings		IMP-ZINC-UPL.21.01
MJ Accessories		IMP-ACC-UPL.21.01

Domestic Products	Multipliers	Price Lists
Utility Fittings		DOM-UPL.21.01
FBE Fittings		DOM-FBE-UPL.21.01
P401 Fittings		DOM-P401-UPL.21.01
Zinc Fittings		DOM-ZINC-UPL.21.01
MJ Accessories		DOM-ACC-UPL.21.01

In addition, we are announcing an approximate Net Price increase for our Municipal Casting Products, effective Monday, February 1, 2021.

Prior committed pricing on 2020 Municipal and Annual Contracts will be honored per our original agreements. All orders received before January 31, 2021, will be price protected for immediate shipment only. We remain committed to earning your business. Thank you for your continued support. We wish you a Happy, Healthy & Safe 2021!

Sincerely,

Jason O'Nan

Jason O'Nan, Vice President
Star® Pipe Products

STAR® PIPE PRODUCTS
4018 WESTHOLLOW PARKWAY HOUSTON, TEXAS 77082-4604
wwww.starpipeproducts.com
T: 281.558.3000
F: 281.558.9000

TÜVRheinland

SP FOUNDRY

EXHIBIT B

TYLER UNION®
Quality Waterworks Products

December 23, 2020

To: All Tyler Union Customers

Re: List Price Increase for Import Restraints Effective February 1st, 2021

Dear Valued Customer,

We are announcing a List Price Increase for our Import Restraint products due to significant inflation in raw materials, ocean freight and other costs of production.

LP2021-NR will be effective February 1st, 2021 with a applicable multiplier for stocking distributors.

Committed pricing on prior 2020 Municipal and Annual Contracts will be honored per the terms of the original agreement. All restraint orders received by January 1st, 2021 for immediate shipment will be price protected.

Import Product	Multiplier	List Price Revision
Joint Restraints		LP2021-NR

Both Excel and PDF files of LP2021-NR are posted to our website, www.tylerunion.com

We thank you for your continued support of Tyler Union and look forward to providing you with quality waterworks products, as we have for nearly 100 years.

Sincerely,

Jerry Jansen

Jerry Jansen
National Sales Manager

EXHIBIT B

TYLER UNION®
Quality Waterworks Products

December 30, 2020

To: All Tyler Union Customers

Re: List Price Increase for Import & Domestic Fittings and Accessories

Dear Valued Customer,

We are announcing pending List Price Increases for our Import & Domestic AWWA Fittings and MJ Accessories due to significant inflation in raw materials, freight, and other costs of production.

Our intent is for the new List Pricing to be effective February 1st, 2021. For your planning purposes, the increase will be approximately:

- % for Domestic Fittings and Accessories
- % for Import Fittings 16" and smaller
- % for Import Fittings 18" and larger
- % for Import Accessories

Applicable regional multipliers will be affirmed at our current Published Multipliers.

We thank you for your continued support of Tyler Union and look forward to providing you with quality waterworks products, as we have for nearly 100 years.

Sincerely,

Jerry Jansen

Jerry Jansen
National Sales Manager

EXHIBIT B

MULTI FITTINGS
HIGHER STANDARDS™

January 15, 2021

SUBJECT: MULTI FITTINGS PRICE INCREASE ANNOUNCEMENT

To our Valued Customers;

Due to repeated raw material cost increases, as well as evolving market conditions, Multi Fittings will implement a price increase (October 1 , 2020 (Current) on **all municipal and plumbing products** effective Monday, March 1, 2021.

New list prices will be available in February at www.multifittings.com and addendum price sheets will follow.

Please call your local representative with any questions.

We thank you for your support.

Sincerely,
Multi Fittings Corporation

Richard St-Aubin, P.Eng.
General Sales Manager - Municipal

EXHIBIT B

TENCATE GEOSYNTHETICS

TENCATE GEOSYNTHETICS

January 11, 2021

Subject: Geosynthetic Price Increase

Dear Valued Partner,

Regrettably, polypropylene market conditions have become even more volatile, which has resulted in additional force majeure announcements from resin suppliers. This volatility is being driven by strong demand and limited raw material supplies on a global scale. This has resulted in raw material pricing increases beyond TenCate Geosynthetics' ability to absorb. As a result, TCG will implement a price increase as follows:

Increase:

- Mirafi® N, E, & S-Series PP nonwovens (i.e., 180N, E1200, S800)
- Mirafi® BXG-Series biaxial PP geogrids (i.e., BXG110, BXG120)
- Mirafi® MPV-Series paving nonwovens (i.e., MPV400, MPV500)
- Mirafi® MPG-Series engineered paving mats & grids (i.e., MPM50E, MPG100)

Increase:

- Mirafi® FW-Series monofilament wovens (i.e., FW404, FW700)
- Mirafi® HP-Series mid-strength wovens (i.e., HP270, HP370, HP570)
- Mirafi® RSi-Series high-strength reinforcement wovens (i.e., RS280i, RS380i, RS580i)
- Miramesh® wovens (GR)
- Mirafi® PT-Series polyester nonwovens (i.e., PT800E, PT1000E, PT1600E)

Increase

- Mirafi® X- Series slit tape wovens (i.e., 500X, 550X, 600X)

Increase

- Miragrid® XT-Series uniaxial PET geogrids (i.e., 3XT, 8XT, 24XT)

**Products not listed above are subject to a price increase if market conditions warrant.*

The price increase will go into effect on February 1, 2021. Orders accepted **and shipped** by January 29, 2021, will be sold at the current price. TCG is unable to accept larger than normal orders and cannot hold pricing past January 29, 2021, due to product availability or warehouse loading time slots. *While this situation is unfortunate, market conditions are such that we must strictly enforce this protocol.*

As we navigate through this volatile time, please stay in close contact with your Regional Sales Manager: provide forecasts and communicate upcoming projects, etc.

Thank you for your business and thank you for your commitment to TenCate Geosynthetics.

Regards,

Todd M. Anderson
Vice President Sales & Marketing

365 South Holland Drive
Pendergrass, GA 30567

Tel 706 693 2226
Tel 888 795 0808

Fax 706 693 4400
www.tencategeo.com

EXHIBIT B

DFW

Product Solutions Innovation, Today and Tomorrow

DFW PLASTICS, INC.

December 29, 2020

To Our Valued Customer:

This letter serves as notice of a price increase on all our product lines effective February 1, 2021. This increase is caused by the continuing rise in cost of raw materials, labor and transportation cost.

You will be able to access the new February 1, 2021 Price List for all product lines after January 20th at www.dfwplasticsinc.com.

All standard orders that ship by January 31st will be invoiced at current pricing levels. All standard orders that ship after February 1st will be subject to the new pricing. All orders based on Quotations will remain as stated in the current quote.

We appreciate your business and look forward to a successful year in 2021. If you have any questions please feel free to contact myself or your local DFW representative.

Best regards,

DFW

Jim McKinnon
VP, Sales & Marketing

PO Box 648 Bedford, TX 76095
P 817.439.3600
F 817.439.3700
www.dfwplasticsinc.com

EXHIBIT B

Hubbell Lenoir City
3621 Industrial Park Dr.
Lenoir City, TN 37771

November 12, 2020

Dear Hubbell Customer,

This past year has proven to be challenging across the industry and we thank you for allowing Hubbell to serve your organization during this difficult time. We take pride in maintaining a safe work environment for all our employees, especially those working in our manufacturing facilities. We continue to be a solutions and logistics provider that customers can rely on for exceptional product, quality and service. The unprecedented adversity brought on by the COVID-19 pandemic undoubtedly pushed all aspects of our business to the limit.

As an essential business, Hubbell incurred significant and unforeseen cost impacts to keep our facilities running, product flowing and our employees safe during the pandemic. The demanding circumstances have also shed light on areas for supply chain enhancement where we are making significant investments to enhance our industry-leading commitment to service and dependability. While we diligently work to minimize the impact of cost pressures on our customers, we must adjust pricing as we enter the new year.

Effective January 1, 2021, we will initiate a price increase of across our product lines. Increases will vary depending on the product, with some falling outside this range at a higher rate of increase. We will implement price adjustments with the following guidelines:

- All Hubbell price lists will be re-issued by 11/25/2020 with an effective date of 1/1/2021.
- Expiring Hubbell blanket quotes will be re-issued by 11/25/2020 with an effective date of 1/1/2021.
- New quotation requests will reflect the above pricing actions.
- Pricing for orders received prior to 12/31/20 for immediate shipment will be honored at the existing quoted prices.
- Hubbell reserves the right to limit order quantities on orders received prior to 12/31/2020.

We recognize the sensitivity of this matter and appreciate your support regarding these pricing actions. If you have any questions, please contact your local Hubbell representative. Thank you for your understanding and continued support of Hubbell.

Sincerely,

Scott D. Martz
VP, General Manager
Hubbell Lenoir City

EXHIBIT B

NAPCO, a Westlake Company
2801 Post Oak Blvd., Suite 600,
Houston, Texas 77056

Tel: 713.840.7473, Fax: 713.552.0087

Date: May 11, 2021

To: All Municipal Customers

From: Brent Wetmore, Vice President - Sales

Subject: PVC Pipe Prices – Municipal Products

NAPCO thanks you for your continued support. We value your business and are committed to being able to accept new orders during this very busy time.

Our increasing backlog is pushing out both our production schedule and our delivery dates. In order to protect ourselves against rising raw material costs, we must increase our current block numbers to the following:

Immediate Shipments: Block 240
(immediate release subject to availability)

All current orders will be honored within terms and are subject to our ability to ship. Orders with expired terms will be re-priced.

If you have any questions regarding product availability or this price increase, please contact your local North American Pipe sales representative.

We appreciate your business and look forward to continuing to serve your PVC pipe needs.

EXHIBIT B

STAR PIPE PRODUCTS

May 3, 2021

To: Our Valued U.S. Customers

RE: **2nd REVISION - List Price Increase for Import Fittings, Accessories & Fabricator Products Effective June 1, 2021**

The unprecedented global supply chain challenges continue to increase our costs. The Chinese Government just rescinded the 13% tax (VAT) credit on most exported Iron & Steel Products effective May 1st, 2021. Therefore, we are rescinding and replacing our April 20th announced price increase for our Import Fittings, Fabricator Products and Accessories product lines.

The revised Price Lists for all Import fittings (including FBE, P401 and Zinc), Accessories and Fabricator Products will be increased 23% from PL21.01. These new Price Lists, to be labeled with a suffix of 21.03, will be posted on our website at www.StarPipeProducts.com shortly. Updated Regional multipliers will also be sent out this week.

All committed inventory that ships before May 31st will be at current pricing and subject to availability. Product shipments after May 31st will be priced off the new PL21.03 with the associated multipliers. This includes backorders from prior orders.

Because of the unforeseen immediate cost increases, we will not be able to honor Municipal or Annual bids that were quoted from PL19.01, or prior lists.

Please contact your Star Territory Manager or Star Inside Sales Representative with details on any approved Municipal or Annual Contracts with Star Pipe Products.

Unfortunately, this is affecting all of us. We apologize for the inconvenience. Thank you for working through it with us.

Sincerely,

Jason O'Nan

Jason O'Nan, Vice President
Star® Pipe Products

STAR® PIPE PRODUCTS
4018 WESTHOLLOW PARKWAY HOUSTON, TEXAS 77082-4604
wwww.starpipeproducts.com
T 281.558.3000
F 281.558.9000

TÜVRheinland

SP FOUNDRY

EXHIBIT B

FORTERRA™

June 14, 2021

Dear Valued Customer,

We at Forterra appreciate the opportunity to serve as your Drainage solutions partner, and we remain committed to providing best-in-class service and the highest quality products. This includes our team's relentless pursuit of decreasing delivery lead times during this surge in construction activity.

As we have previously communicated, the unprecedented demand for steel, cement, freight and other raw materials continues to drive the inputs for our products to extraordinary levels. As an example, our steel suppliers have just announced a fourth increase this year and are signaling another increase for this Summer.

While we are taking daily action to minimize the pass-through impacts to you, Forterra must raise pricing on our products. Effective July 15, 2021 our prices will increase by 14%.

Current market conditions also make it necessary to update our Terms & Conditions. Existing quotes will be honored for 30-days. And, purchase orders received after July 15 will be honored for 60-days, after which, are subject to fluctuation in price.

Forecasts show no signs of these material rate hikes slowing down. As such, we will notify you in August with updates on the inflation of our input costs and what our pricing intentions will be effective October 1st.

Thank you for your business and the opportunity to partner with you on your projects. Please contact your Sales Manager with any project specific questions, or you may reach me directly @ 1-502-594-1321

Sincerely,

Jim Nanfeldt

Jim Nanfeldt
Florida General Manager
Forterra Pipe & Precast

stellar

City of Jacksonville Fire Station 65
Subcontractor Bid Status Report

11/1/2021

Fire Station 65 - City of Jacksonville

BID PACKAGES | MESSAGES | FILES | INFORMATION | BID FORMS | TEAM | REPORTS

Overall Project Reach

105	72%	76	79%	60	92%	55
COMPANIES		VIEWED		BIDDING		BIDS

Company	Enterprise Type	Bid Package	Bidding Status
Allsite Contracting, Inc.	Small Business Enterprise (SBE)	Sitework, Paving & Underground Utilities	BID_SUBMITTED
Dirt Works		Sitework, Paving & Underground Utilities	BID_SUBMITTED
DNS Contracting		Sitework, Paving & Underground Utilities	BID_SUBMITTED
4K Construction		Sitework, Paving & Underground Utilities	NOT_BIDDING
Petticoat Schmitt Civil Contractors, Inc.	Other	Sitework, Paving & Underground Utilities	NOT_BIDDING
Sunstate Nursery & Landscaping	None	Landscape	NOT_BIDDING
Tree Amigos		Landscape	BID_SUBMITTED
Costa Verde Lands, LLC	Other	Landscape	BID_SUBMITTED
Birken Construction	JSEB Small Business Enterprise (SBE)	Concrete	BID_SUBMITTED
Jims Concrete of Brevard, Inc.	None	Concrete	BID_SUBMITTED
Mallen Construction	Other	Concrete	NO BID
A A Pittman & Sons Concrete, Inc.	None	Concrete	BID_SUBMITTED
Capital Concrete & Masonry Solutions		Masonry	NOT_BIDDING
EK Birken Masonry	JSEB Small Business Enterprise (SBE)	Masonry	BID_SUBMITTED
R.D. Masonry, INC.	None	Masonry	NOT_BIDDING
Stoddard Masonry, Inc.	Other	Masonry	BID_SUBMITTED
R J Tripp Inc. dba J L Tripp Builders	None	Masonry	NOT_BIDDING
Allstate Steel Company	Women Business Enterprise (WBE), Other	Structural & Miscellaneous Metals & Bollarc	NOT_BIDDING
Fabco Metal Products	None	Structural & Miscellaneous Metals & Bollarc	BID_SUBMITTED
Trinity Fabricators	Women Business Enterprise (WBE), None	Structural & Miscellaneous Metals & Bollarc	NOT_BIDDING
Whitley Steel Co. Inc.	Other, None	Structural & Miscellaneous Metals & Bollarc	NOT_BIDDING
Jacksonville Steel Products, Inc.	None	Structural & Miscellaneous Metals & Bollarc	BID_SUBMITTED
Craggs Glass		Aluminum Windows, Storefront Doors & Gl	BID_SUBMITTED
Ace Door and Window	None	Aluminum Windows, Storefront Doors & Gl	NO_BID
Brad's Glass Company	None	Aluminum Windows, Storefront Doors & Gl	NO_BID
Lee & Cates Glass	None	Aluminum Windows, Storefront Doors & Gl	NOT_BIDDING
Capitol Glass & Aluminum	None	Aluminum Windows, Storefront Doors & Gl	BID_SUBMITTED
Register Roofing Sheet Metal, Inc.	Small Business Enterprise (SBE)	Roof, Gutters & Downspouts, Facia & Trim	BID_SUBMITTED
Stonebridge Construction Services, LLC	None	Roof, Gutters & Downspouts, Facia & Trim	NOT_BIDDING
BBG Contracting Group, Inc.		Roof, Gutters & Downspouts, Facia & Trim	NOT_BIDDING
Perry Roofing Contractors	None	Roof, Gutters & Downspouts, Facia & Trim	NOT_BIDDING
Childers Roofing & Sheetmetal	None, Other	Roof, Gutters & Downspouts, Facia & Trim	NOT_BIDDING
Reliant Roofing, Inc.	None, Small Business Enterprise (SBE)	Roof, Gutters & Downspouts, Facia & Trim	BID_SUBMITTED
Alpha House Construction, Inc	None	Roof, Gutters & Downspouts, Facia & Trim	BID_SUBMITTED
American Insulators, LLC	Other, None	Spray Foam Insulation	NOT_BIDDING
KirbyCo Builders, Inc.	None	Spray Foam Insulation	BID_SUBMITTED
Builders First Source - ProBuild	Other, None	Roof Trusses & Sheathing	NOT_BIDDING
KirbyCo Builders, Inc.	None	Roof Trusses & Sheathing	BID_SUBMITTED
KirbyCo Builders, Inc.	None	Framing, Drywall, FRP, Insulation & Rough C	BID_SUBMITTED
KirbyCo Builders, Inc.	None	Acoustical Grid Ceilings	BID_SUBMITTED
USI First Choice	None	Spray Foam Insulation	BID_SUBMITTED
J.E. Abercrombie, Inc.	None	Spray Foam Insulation	NOT_BIDDING
J.E. Abercrombie, Inc.	None	Roof Trusses & Sheathing	NOT_BIDDING
J.E. Abercrombie, Inc.	None	Framing, Drywall, FRP, Insulation & Rough C	BID_SUBMITTED
J.E. Abercrombie, Inc.	None	Acoustical Grid Ceilings	BID_SUBMITTED
Southern Foam Insulation, Inc.	None	Spray Foam Insulation	BID_SUBMITTED
Tailored Foam of Florida, LLC.	Other	Spray Foam Insulation	BID_SUBMITTED
Lasa Construction, Inc.	Minority Business Enterprise (MBE), Disadvantaged B	Spray Foam Insulation	BIDDING
Lasa Construction, Inc.	Minority Business Enterprise (MBE), Disadvantaged B	Roof Trusses & Sheathing	NOT_BIDDING
Lasa Construction, Inc.	Minority Business Enterprise (MBE), Disadvantaged B	Framing, Drywall, FRP, Insulation & Rough C	BID_SUBMITTED
Lasa Construction, Inc.	Minority Business Enterprise (MBE), Disadvantaged B	Acoustical Grid Ceilings	BID_SUBMITTED
Lasa Construction, Inc.	Minority Business Enterprise (MBE), Disadvantaged B	Paint & Caulk	NOT_BIDDING
B&H Interiors		Spray Foam Insulation	NOT_BIDDING

B&H Interiors		Roof Trusses & Sheathing	NOT_BIDDING
B&H Interiors		Framing, Drywall, FRP, Insulation & Rough C	BID_SUBMITTED
B&H Interiors		Acoustical Grid Ceilings	NOT_BIDDING
Manning Building Supplies		Roof Trusses & Sheathing	BID_SUBMITTED
Benchmark Commercial Services, LLC	Small Business Enterprise (SBE)	Millwork, Cabinets & Trim, Bunker Gear Sto	NOT_BIDDING
Antique & Modern Cabinets		Millwork, Cabinets & Trim, Bunker Gear Sto	BID_SUBMITTED
Riverview Millworks, Inc.	Small Business Enterprise (SBE)	Millwork, Cabinets & Trim, Bunker Gear Sto	BID_SUBMITTED
Doerr's Custom Cabinets & Trim LLC	None	Millwork, Cabinets & Trim, Bunker Gear Sto	BID_SUBMITTED
IR Bowen (SE Stainless)		Stainless Steel Cabinets & Countertops	BID_SUBMITTED
Ray Ware Hardware	None	Doors, Frames & Hardware	BID_SUBMITTED
Taylor Cotton & Ridley	Small Business Enterprise (SBE)	Doors, Frames & Hardware	NOT_BIDDING
Cook & Boardman	Disadvantaged Business Enterprise (DBE), Other,	Doors, Frames & Hardware	BID_SUBMITTED
Cook & Boardman	Disadvantaged Business Enterprise (DBE), Other,	Signage, Plaques & Lettering	NOT_BIDDING
Cook & Boardman	Disadvantaged Business Enterprise (DBE), Other,	Fire Extinguishers & Cabinets	NOT_BIDDING
Cook & Boardman	Disadvantaged Business Enterprise (DBE), Other,	Flagpoles & Accessories	NOT_BIDDING
Cook & Boardman	Disadvantaged Business Enterprise (DBE), Other,	Toilet Partitions & Accessories	NOT_BIDDING
American Roll Up Door Company	Small Business Enterprise (SBE)	Sectional Overhead Doors (Non-Insulated)	BID_SUBMITTED
Rite Hite Co. LLC / Arbon Equipment Corpora	None	Sectional Overhead Doors (Non-Insulated)	BID_SUBMITTED
Miner Corporation	None, Small Business Enterprise (SBE), Other	Sectional Overhead Doors (Non-Insulated)	NO_BID
Dixie Contract Carpet, Inc.	Disabled Veteran Business Enterprise (DVBE)	Ceramic Tile Floors & Walls, Sheet Rubber F	BID_SUBMITTED
Shaw Contract Flooring Services, Inc. dba Spi	Other, None	Ceramic Tile Floors & Walls, Sheet Rubber F	BID_SUBMITTED
Acousti Engineering Company	None	Ceramic Tile Floors & Walls, Sheet Rubber F	BID_SUBMITTED
Acousti Engineering Company	None	Acoustical Grid Ceilings	NOT_BIDDING
S. David Flooring, LLC	Minority Business Enterprise (MBE), Other	Ceramic Tile Floors & Walls, Sheet Rubber F	BID_SUBMITTED
Birken Flooring	JSEB	Ceramic Tile Floors & Walls, Sheet Rubber F	NOT_BIDDING
Belets Painting & Maintenance, Inc.	None	Paint & Caulk	BID_SUBMITTED
S. David & Company, LLC	Other	Paint & Caulk	BID_SUBMITTED
Dave Motta Painting	None	Paint & Caulk	NO_BID
Commercial Specialties, LLC	Minority Business Enterprise (MBE)	Signage, Plaques & Lettering	BID_SUBMITTED
Commercial Specialties, LLC	Minority Business Enterprise (MBE)	Fire Extinguishers & Cabinets	BID_SUBMITTED
Commercial Specialties, LLC	Minority Business Enterprise (MBE)	Flagpoles & Accessories	BID_SUBMITTED
Commercial Specialties, LLC	Minority Business Enterprise (MBE)	Toilet Partitions & Accessories	BID_SUBMITTED
George Coyle & Sons	Small Business Enterprise (SBE)	Signage, Plaques & Lettering	BID_SUBMITTED
George Coyle & Sons	Small Business Enterprise (SBE)	Toilet Partitions & Accessories	BID_SUBMITTED
Holman, Inc.	Minority Business Enterprise (MBE), Women Business	Fire Extinguishers & Cabinets	BID_SUBMITTED
Holman, Inc.	Minority Business Enterprise (MBE), Women Business	Toilet Partitions & Accessories	BID_SUBMITTED
Hollman, Inc.	Small Business Enterprise (SBE), Disadvantaged Busin	Wood Lockers	BID_SUBMITTED
Ideal Lockers Inc.		Wood Lockers	NOT_BIDDING
Bender & Modlin Fire Sprinkler, Inc.	Small Business Enterprise (SBE)	Fire Protection System	BID_SUBMITTED
Cox Fire Protection, Inc.	Minority Business Enterprise (MBE), Small Business Er	Fire Protection System	BID_SUBMITTED
Aegis Fire Protection	Minority Business Enterprise (MBE)	Fire Protection System	NOT_BIDDING
Wiginton Fire Systems	None	Fire Protection System	BID_SUBMITTED
Gary Rodgers Plumbing Company, Inc.	None	Plumbing & Fixtures	BID_SUBMITTED
Touchton Plumbing Contractors, Inc.	Small Business Enterprise (SBE)	Plumbing & Fixtures	BID_SUBMITTED
Campbell Plumbing & Mechanical Contractor	None	Plumbing & Fixtures	BIDDING
Campbell Plumbing & Mechanical Contractor	None	HVAC, Diesel Exhaust System & Kitchen Exh	BIDDING
Bill Williams Air Conditioning & Heating, Inc.	Women Business Enterprise (WBE)	HVAC, Diesel Exhaust System & Kitchen Exh	BID_SUBMITTED
Weather Engineers, Inc.	None	HVAC, Diesel Exhaust System & Kitchen Exh	BID_SUBMITTED
AC General, Inc.	Other	HVAC, Diesel Exhaust System & Kitchen Exh	NOT_BIDDING
AEC Electric		Electrical, LV & Security, Communications, S	NOT_BIDDING
American Electrical Contracting, Inc.	None	Electrical, LV & Security, Communications, S	BID_SUBMITTED
MetroPower	Other, None	Electrical, LV & Security, Communications, S	BID_SUBMITTED
Coastal Electric Co. of Florida	None	Electrical, LV & Security, Communications, S	BID_SUBMITTED
Southeast Window Covering	Disabled Veteran Business Enterprise (DVBE)	Horizontal Louver Blinds	NOT_BIDDING
Interior Specialties	None	Horizontal Louver Blinds	NOT_BIDDING
Well Kept Windows	None	Horizontal Louver Blinds	BID_SUBMITTED
Marietta Drapery & Window Coverings, Inc.	Small Business Enterprise (SBE), None, Other	Horizontal Louver Blinds	NOT_BIDDING
Workplace Solutions, Inc.		Horizontal Louver Blinds	NOT_BIDDING
Armstrong Fence Company	Small Business Enterprise (SBE)	Chain Link Fences & Gates, Motorized Gates	NOT_BIDDING
Newsome Fence Co., Inc.	Other	Chain Link Fences & Gates, Motorized Gates	NOT_BIDDING
All Out Fence Inc.	None	Chain Link Fences & Gates, Motorized Gates	NOT_BIDDING
Frontline Fencing Inc	Small Business Enterprise (SBE)	Chain Link Fences & Gates, Motorized Gates	BID_SUBMITTED
Duval Fence	None	Chain Link Fences & Gates, Motorized Gates	BID_SUBMITTED
Superior Fence & Rail	Disabled Veteran Business Enterprise (DVBE)	Chain Link Fences & Gates, Motorized Gates	BID_SUBMITTED

EXHIBIT B

JACKSONVILLE
Daily Record

PROOF OF PUBLICATION

(Published daily except Saturday, Sunday and legal holidays)
Jacksonville, Duval County, Florida

STATE OF FLORIDA,

S.S.

COUNTY OF DUVAL,

Before the undersigned authority personally appeared Rhonda Fisher, who on oath says that she is the Publisher's Representative of JACKSONVILLE DAILY RECORD, a daily (except Saturday, Sunday and legal holidays) newspaper published at Jacksonville, in Duval County, Florida; that the attached copy of advertisement, being a Request for Proposals

in the matter of Fire Station 65

in the Court of Duval County, Florida, was published in said newspaper in the issues of 10/18/21, 10/19/21, 10/20/21, 10/21/21, 10/22/21, 10/25/21, 10/26/21, 10/27/21

Affiant further says that the said JACKSONVILLE DAILY RECORD is a newspaper at Jacksonville, in said Duval County, Florida, and that the said newspaper has heretofore been continuously published in said Duval County, Florida, each day (except Saturday, Sunday and legal holidays) and has been entered as periodicals matter at the post office in Jacksonville, in said Duval County, Florida, for a period of one year next preceding the first publication of the attached copy of advertisement; and affiant further says that she has neither paid nor promised any person, firm or corporation any discount, rebate, commission or refund for the purpose of securing this advertisement for publication in said newspaper.
*This notice was placed on the newspaper's website and floridapublicnotices.com on the same day the notice appeared in the newspaper.

Rhonda Fisher

Sworn to and subscribed before me this 27th day of October, 2021 A.D. by Rhonda Fisher who is personally known to me.

JANET WEINEL
Notary Public, State of Florida
My Comm. Expires 12/18/2024
Commission No. HH056417

Notary Signature

Seal

Notary Public, State of Florida

REQUEST FOR PROPOSALS
Stellar is soliciting subcontractor proposals for the new City of Jacksonville Fire Station 65. Trades needed include sitework, concrete, masonry, wood trusses, drywall/acoustical, finishes, and MEP. Proposals are due to Stellar no later than October 27, 2021. Please contact Scott Wright at swright@stellar.net for additional information.
Oct. 18/19/20/21/
22/25/26/27 00 (21-07066D)

SUBJECT: RFQ-DESIGN-BUILD SERVICES FIRE STATIONS NUMBERS: 36, 64, AND 65

BID # CDB-0127-19

OPEN DATE: 04/17/2019

COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
CONSTRUCTION – DESIGN/BUILD- REQUEST FOR QUALIFICATIONS

AGENCY: DEPARTMENT OF PUBLIC WORKS

BASIS OF AWARD: EVALUATION CRITERIA

NUMBER OF BIDS INVITED: 5 NUMBER RECEIVED: 6 OTHER: 0

SUMMARY OF BIDS AND RECOMMENDED ACTIONS:

The Department of Public Works has completed negotiations with Stellar Group, Inc., for the Design Build Services for Fire Stations Numbers 36, 64, and 65.

Recommend approval of award to Stellar Group, Inc. to provide 90% design and preconstruction services for Fire Station No. 65. This incorporates the scope & fee summary, Exhibit "A" and requires a total estimated design time of 213 days from the Notice to Proceed. Total guaranteed maximum price not-to-exceed $241,309.11.

Funding for this award is to be executed by Amendment 1A and encumbered by account: 004335.565031.1.32111.384020 to be executed by contract change order through Office of General Counsel

Attachments: Recommendation Memo, Exhibit "A", Previous Award(s)

BUYER Nekole Hulitt
NEKOLE HULITT

RESPECTFULLY SUBMITTED
GREGORY PEASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: John P. Pappas, P.E., Director, Public Works Department

(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING 0 DATE: 4/22/2021

OTHER

ACTION OF AWARDING AUTHORITY DATE 4/26/2021

APPROVED ✓ DISAPPROVED:

OTHER:

SIGNATURE OF AUTHENTICATION

SUBJECT: RFQ-DESIGN-BUILD SERVICES FIRE STATION#S: 36, 64 AND 65

BID # CDB-0127-19

OPEN DATE: 04/17/2019

COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
CONSTRUCTION – DESIGN/BUILD- REQUEST FOR QUALIFICATIONS

AGENCY: DEPARTMENT OF PUBLIC WORKS

BASIS OF AWARD: EVALUATION CRITERIA

NUMBER OF BIDS INVITED: 5 NUMBER RECEIVED: 5 OTHER: 0

SUMMARY OF BIDS AND RECOMMENDED ACTIONS:
Subject bid was previously shortlisted for three firms and approved on 06/27/19; Interviews were held for the three shortlisted firms based on the final average scores, the following firms are listed alphabetically. The ranking of first, second and third designates the order of qualification of these firms to perform the required services:

2) Auld & White Constructors- 119.75
1) Stellar Group, Inc. - 128.50
3) The Haskell Group- 119.50

Pursuant to Section 2.6 – Award of Contract of the RFP, recommend approval for final list to begin negotiations with number one ranked firm Stellar Group, Inc.

Attachments: Recommendation Memo, Scoring Matrix, Section 2.6, Previous Award

BUYER Marilyn Laidler
MARILYN LAIDLER

RESPECTFULLY SUBMITTED
GREGORY PEASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: John P. Pappas, P.E., Director, Public Works Department

(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING Ø DATE: 8/08/19

Teresa R Eichman

OTHER

ACTION OF AWARDING AUTHORITY DATE 8/8/19

APPROVED ✓ DISAPPROVED:

OTHER:

SIGNATURE OF AUTHENTICATION

Brian Hughes
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of:

SUBJECT: RFQ-DESIGN-BUILD SERVICES FIRE STATION#S: 36, 64 AND 65

BID # CDB-0127-19

OPEN DATE: 04/17/2019

COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
CONSTRUCTION – DESIGN/BUILD- REQUEST FOR QUALIFICATIONS

AGENCY: DEPARTMENT OF PUBLIC WORKS

BASIS OF AWARD: EVALUATION CRITERIA

NUMBER OF BIDS INVITED: 5 NUMBER RECEIVED: 5 OTHER: 0

SUMMARY OF BIDS AND RECOMMENDED ACTIONS:
Recommend approval to reject Hager Construction Company for not meeting the minimum requirement of completing a vertical project with a minimum cost of $2,500,000.00 within the last five (5) years.

The remaining five (5) proposals received for evaluation were found to be responsive, interested, qualified and available to provide the services required by the RFP. Based on the above the following firms listed alphabetically were determined to be the most qualified. The ranking of first, second and third designates the order of qualification of these firms to perform the required services:

3) Auld & White Constructors- 92.75
2) The Haskell Company- 95.00
1) The Stellar Group- 98.50

Pursuant to Section 2.6 – Award of Contract of the RFP, recommend approval to move forward to presentation/interviews before CSPEC.

Attachments: Recommendation Memo, Scoring Matrix, Bid Tabulation, Vendor Rejection Letter/Email, Section 2.6

BUYER Marilyn Laidler
MARILYN LAIDLER

RESPECTFULLY SUBMITTED
GREGORY PEASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: Robin G. Smith, P.E., Chief, Engineering & Construction Management

(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING Ø DATE: 6/27/19

OTHER

ACTION OF AWARDING AUTHORITY DATE 6/27/19

APPROVED DISAPPROVED:

OTHER:

SIGNATURE OF AUTHENTICATION

Sam E. Mousa
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of:
Executive Order No. 2013-05
